
Stack CNR-1 - 6in XR35 corners

8 blanks, 8 pieces | 1 layers | FB courses 1-2 | stack height 607 mm of 1300 mm cap

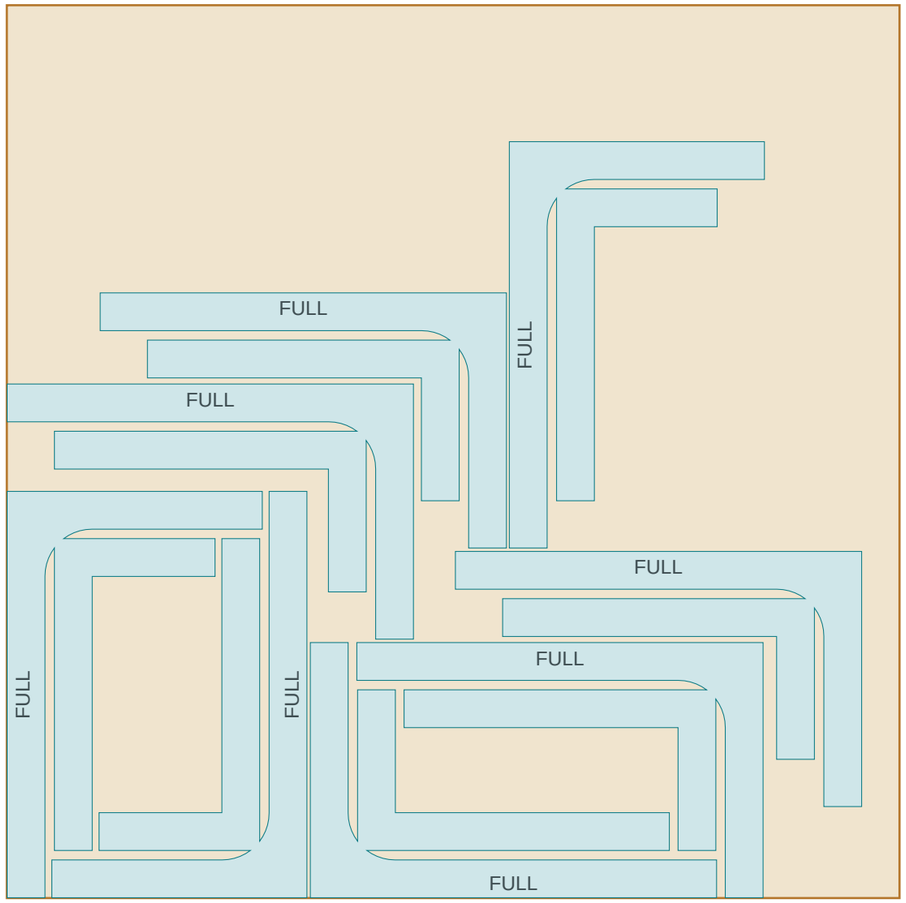

LAYER 1 - FB courses 1-2
8 blanks, 8 pieces


PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - FB courses 1-2 (place first)

- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner

Checked by _____

Date _____

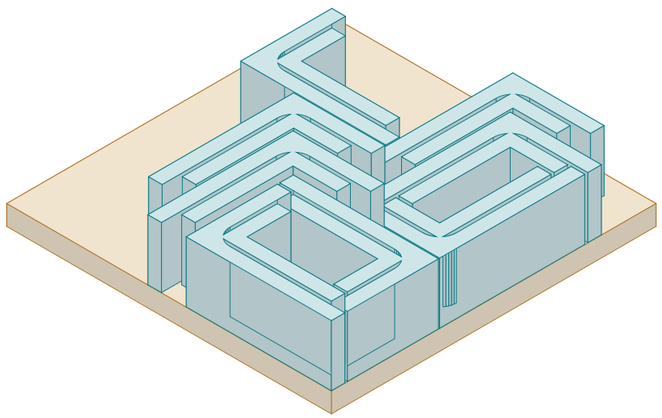

Nudura™

PALLET STACK SHEET


CNR-1

Plan view, top layer first - build from the bottom up


PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	**LAYERS**	1
SERIES	6in XR35	**HEIGHT**	607 mm
FORMS	8	**PALLET**	2400 x 2400

Stack CUT-1 - 6in XR35 straights


25 blanks, 41 pieces | 5 layers | FB courses 1-2 | stack height 1293 mm of 1300 mm cap

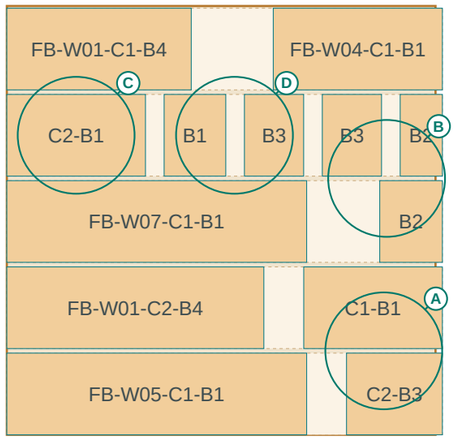


LAYER 5 - FB courses 1-2
5 blanks, 13 pieces

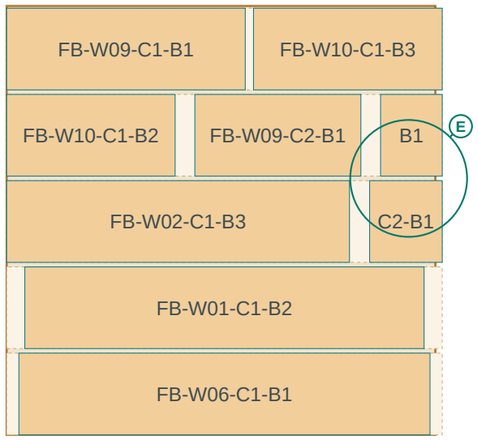


LAYER 4 - FB courses 1-2
5 blanks, 9 pieces

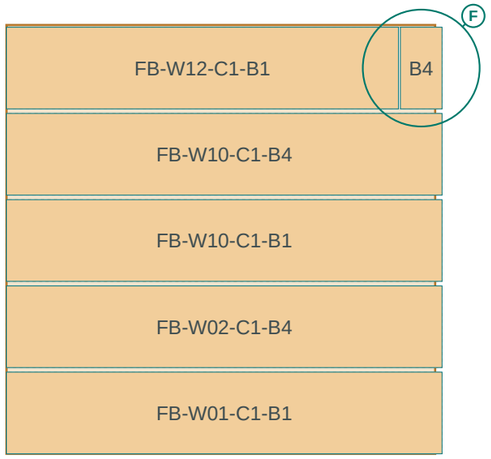

LAYER 3 - FB courses 1-2
5 blanks, 6 pieces

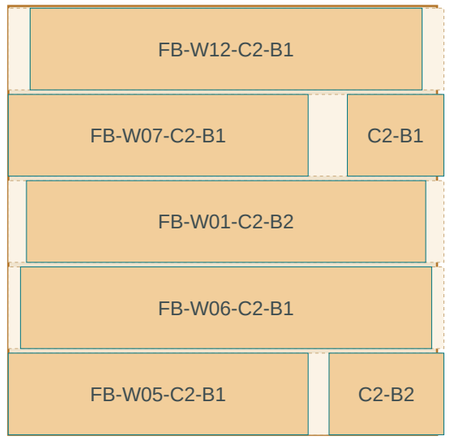

LAYER 2 - FB course 2
5 blanks, 7 pieces

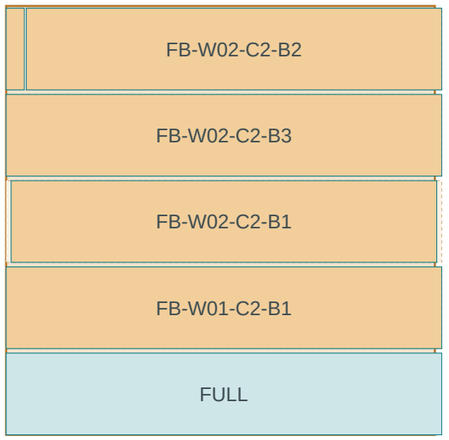

LAYER 1 - FB course 2
5 blanks, 6 pieces

ISOMETRIC 5 layers, built bottom up

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - FB course 2 (place first)
- ☐ FULL form
- ☐ FB-W01-C2-B1
- ☐ FB-W02-C2-B1
- ☐ FB-W02-C2-B3
- ☐ FB-W10-C2-B6
- ☐ FB-W02-C2-B2

LAYER 2 - FB course 2
- ☐ FB-W05-C2-B1
- ☐ FB-W08-C2-B2
- ☐ FB-W06-C2-B1
- ☐ FB-W01-C2-B2
- ☐ FB-W07-C2-B1
- ☐ FB-W04-C2-B1
- ☐ FB-W12-C2-B1

LAYER 3 - FB courses 1-2
- ☐ FB-W01-C1-B1
- ☐ FB-W02-C1-B4
- ☐ FB-W10-C1-B1
- ☐ FB-W10-C1-B4
- ☐ FB-W12-C1-B1
- ☐ FB-W10-C2-B4

LAYER 4 - FB courses 1-2
- ☐ FB-W06-C1-B1
- ☐ FB-W01-C1-B2
- ☐ FB-W02-C1-B3
- ☐ FB-W10-C2-B1
- ☐ FB-W10-C1-B2
- ☐ FB-W09-C2-B1
- ☐ FB-W03-C1-B1
- ☐ FB-W09-C1-B1
- ☐ FB-W10-C1-B3

LAYER 5 - FB courses 1-2
- ☐ FB-W05-C1-B1
- ☐ FB-W10-C2-B3
- ☐ FB-W01-C2-B4
- ☐ FB-W11-C1-B1
- ☐ FB-W07-C1-B1
- ☐ FB-W02-C1-B2
- ☐ FB-W11-C2-B1
- ☐ FB-W03-C2-B1
- ☐ FB-W01-C1-B3
- ☐ FB-W01-C2-B3
- ☐ FB-W08-C1-B2
- ☐ FB-W01-C1-B4

LAYER 5 - FB courses 1-2 (continued)
- ☐ FB-W04-C1-B1

Checked by _____

Date _____

DETAIL A
layer 5, 2x

DETAIL C
layer 5, 2x

DETAIL E
layer 4, 2x

DETAIL B
layer 5, 2x

DETAIL D
layer 5, 2x

DETAIL F
layer 3, 2x

Pieces without a detail here: see the placement checklist (3)


Nudura™ **PALLET STACK SHEET** **CUT-1**

Plan view, top layer first - build from the bottom up


PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	5
SERIES	6in XR35	HEIGHT	1293 mm
FORMS	25	PALLET	2400 x 2400

Stack FULL-1 - 6in XR35 straights

6 blanks, 6 pieces | 2 layers | FB courses 1-2 | stack height 607 mm of 1300 mm cap



LAYER 2 - FB course 2
1 blanks, 1 pieces

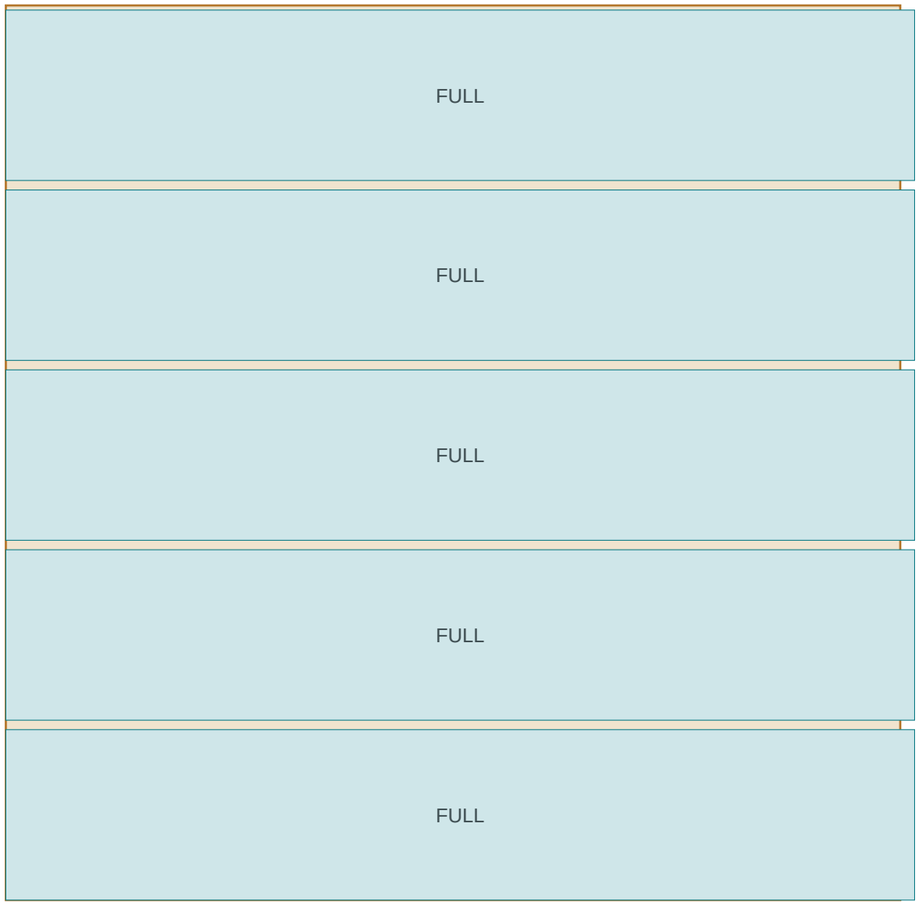

LAYER 1 - FB courses 1-2
5 blanks, 5 pieces

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - FB courses 1-2 (place first)


- ☐ FULL form
- ☐ FULL form
- ☐ FULL form
- ☐ FULL form
- ☐ FULL form

LAYER 2 - FB course 2

- ☐ FULL form

Checked by _____

Date _____

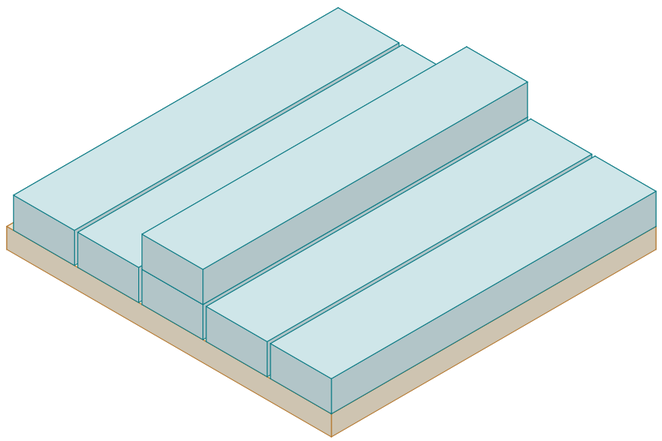


Nudura™ **PALLET STACK SHEET** **FULL-1**

Plan view, top layer first - build from the bottom up


PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	2
SERIES	6in XR35	HEIGHT	607 mm
FORMS	6	PALLET	2400 x 2400

Stack CNR-2 - 6in XR35 corners


24 blanks, 24 pieces | 2 layers | L1 courses 1-6 | stack height 1064 mm of 1300 mm cap

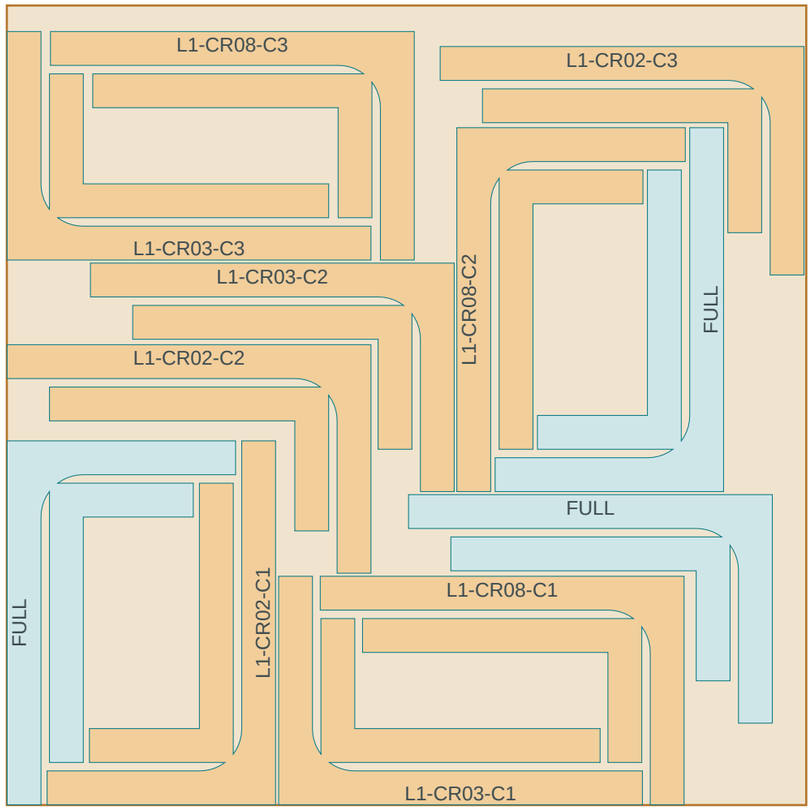

LAYER 2 - L1 courses 1-3
12 blanks, 12 pieces

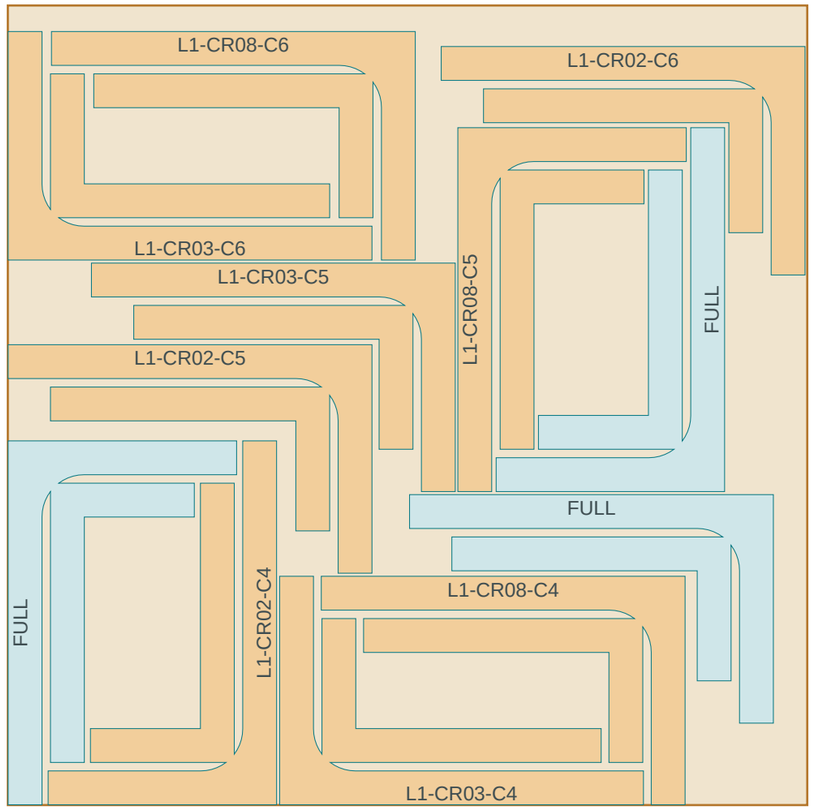

LAYER 1 - L1 courses 4-6
12 blanks, 12 pieces

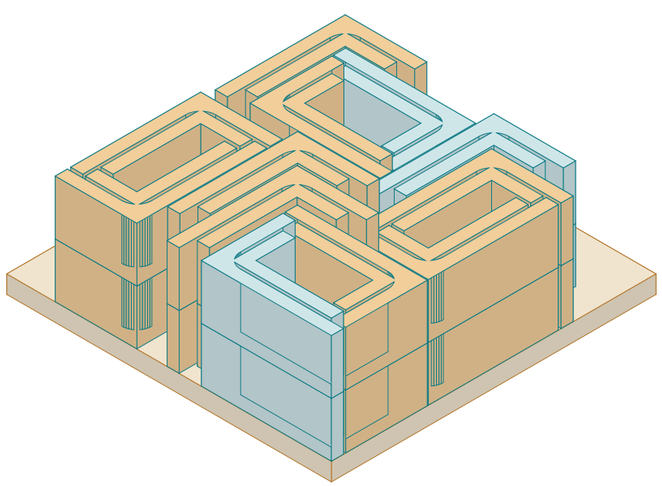

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L1 courses 4-6 (place first)

- ☐ FULL corner
- ☐ L1-CR02-C4
- ☐ L1-CR03-C4
- ☐ L1-CR08-C4
- ☐ FULL corner
- ☐ L1-CR02-C5
- ☐ L1-CR03-C5
- ☐ L1-CR08-C5
- ☐ FULL corner
- ☐ L1-CR02-C6
- ☐ L1-CR03-C6
- ☐ L1-CR08-C6

LAYER 2 - L1 courses 1-3

- ☐ FULL corner
- ☐ L1-CR02-C1
- ☐ L1-CR03-C1
- ☐ L1-CR08-C1
- ☐ FULL corner
- ☐ L1-CR02-C2
- ☐ L1-CR03-C2
- ☐ L1-CR08-C2
- ☐ FULL corner
- ☐ L1-CR02-C3
- ☐ L1-CR03-C3

LAYER 2 - L1 courses 1-3 (continued)

- ☐ L1-CR08-C3

Checked by _____

Date _____

Nudura™

PALLET STACK SHEET


CNR-2

Plan view, top layer first - build from the bottom up


PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	2
SERIES	6in XR35	HEIGHT	1064 mm
FORMS	24	PALLET	2400 x 2400

Stack CUT-2 - 6in XR35 straights


25 blanks, 45 pieces | 5 layers | L1 courses 1-7 | stack height 1293 mm of 1300 mm cap

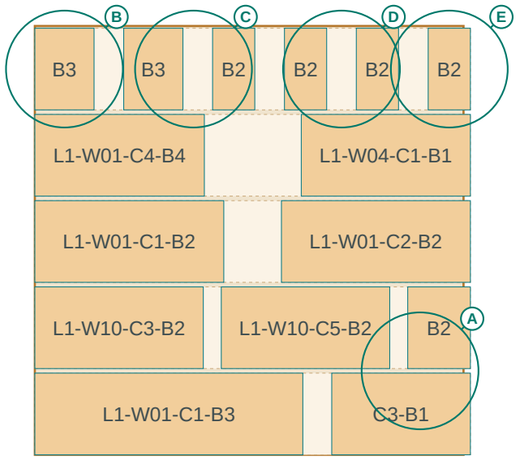


LAYER 5 - L1 courses 1-7
5 blanks, 15 pieces

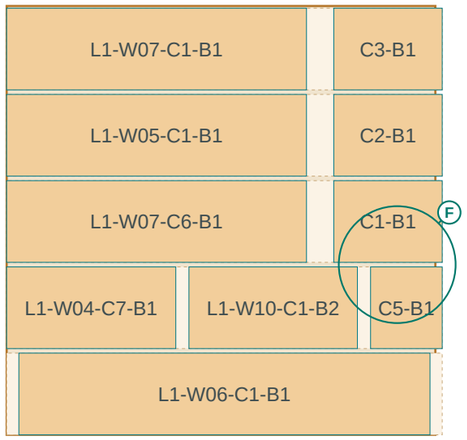


LAYER 4 - L1 courses 1, 2, 3, 5, 6, 7
5 blanks, 10 pieces

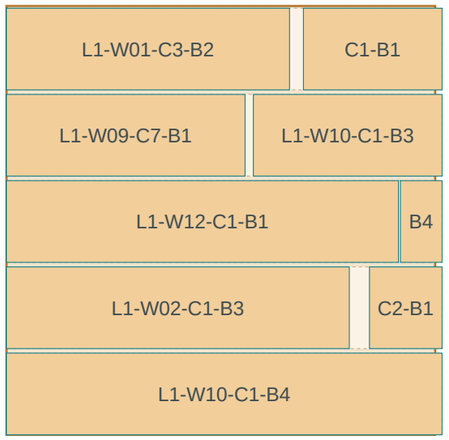


LAYER 3 - L1 courses 1, 2, 3, 7
5 blanks, 9 pieces

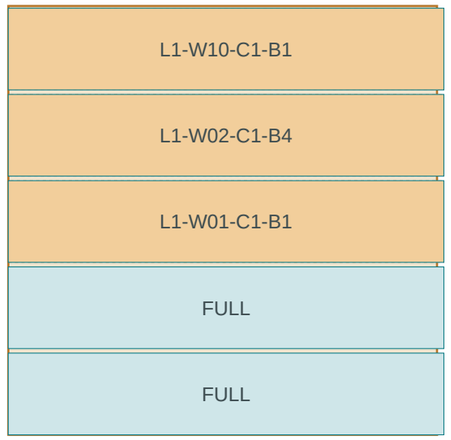

LAYER 2 - L1 course 1
5 blanks, 5 pieces

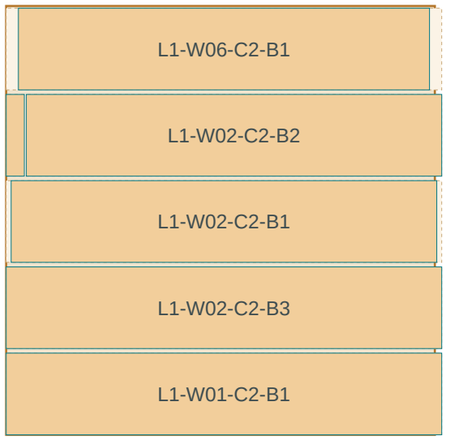

LAYER 1 - L1 course 2
5 blanks, 6 pieces

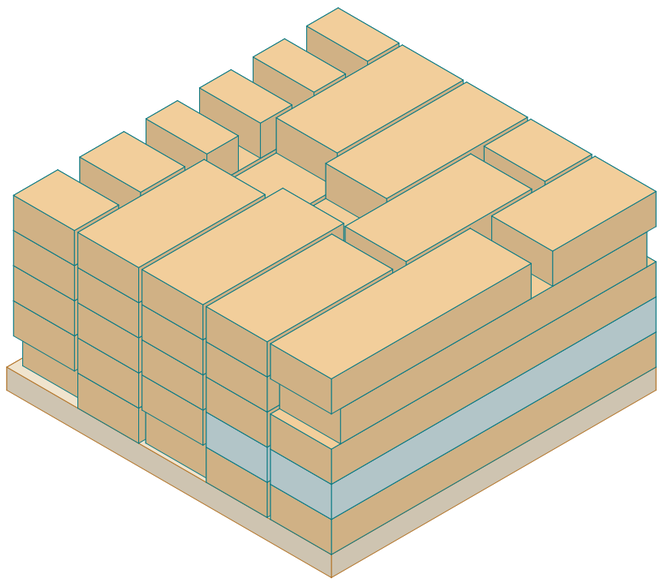

ISOMETRIC 5 layers, built bottom up

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L1 course 2 (place first)
- ☐ L1-W01-C2-B1
- ☐ L1-W02-C2-B3
- ☐ L1-W02-C2-B1
- ☐ L1-W10-C2-B6
- ☐ L1-W02-C2-B2
- ☐ L1-W06-C2-B1

LAYER 2 - L1 course 1
- ☐ FULL form
- ☐ FULL form
- ☐ L1-W01-C1-B1
- ☐ L1-W02-C1-B4
- ☐ L1-W10-C1-B1

LAYER 3 - L1 courses 1, 2, 3, 7
- ☐ L1-W10-C1-B4
- ☐ L1-W02-C1-B3
- ☐ L1-W10-C2-B1
- ☐ L1-W12-C1-B1
- ☐ L1-W10-C2-B4
- ☐ L1-W09-C7-B1
- ☐ L1-W10-C1-B3
- ☐ L1-W01-C3-B2
- ☐ L1-W11-C1-B1


LAYER 4 - L1 courses 1, 2, 3, 5, 6, 7
- ☐ L1-W06-C1-B1
- ☐ L1-W04-C7-B1
- ☐ L1-W10-C1-B2
- ☐ L1-W07-C5-B1
- ☐ L1-W07-C6-B1
- ☐ L1-W09-C1-B1
- ☐ L1-W05-C1-B1
- ☐ L1-W09-C2-B1
- ☐ L1-W07-C1-B1
- ☐ L1-W09-C3-B1

LAYER 5 - L1 courses 1-7
- ☐ L1-W01-C1-B3
- ☐ L1-W11-C3-B1
- ☐ L1-W10-C3-B2
- ☐ L1-W10-C5-B2
- ☐ L1-W02-C1-B2
- ☐ L1-W01-C1-B2
- ☐ L1-W01-C2-B2
- ☐ L1-W01-C4-B4
- ☐ L1-W04-C1-B1
- ☐ L1-W01-C7-B3


LAYER 5 - L1 courses 1-7 (continued)
- ☐ L1-W01-C6-B3
- ☐ L1-W08-C1-B2
- ☐ L1-W08-C3-B2
- ☐ L1-W08-C5-B2
- ☐ L1-W08-C7-B2

Checked by _____


Date _____




DETAIL A
layer 5, 2x




DETAIL C
layer 5, 2x




DETAIL E
layer 5, 2x



DETAIL B
layer 5, 2x



DETAIL D
layer 5, 2x



DETAIL F
layer 4, 2x

Pieces without a detail here: see the placement checklist (4)

Nudura™

PALLET STACK SHEET


CUT-2

Plan view, top layer first - build from the bottom up


PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	5
SERIES	6in XR35	HEIGHT	1293 mm
FORMS	25	PALLET	2400 x 2400

Stack CUT-3 - 6in XR35 straights


25 blanks, 58 pieces | 5 layers | L1 courses 2-7 | stack height 1293 mm of 1300 mm cap

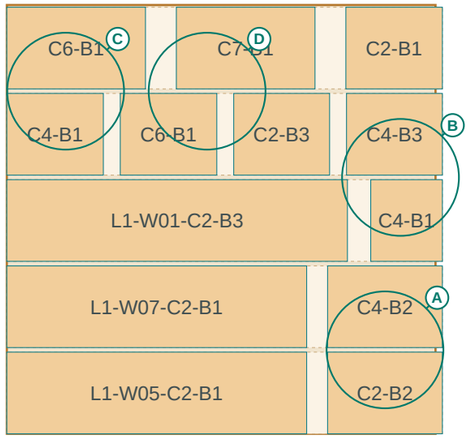


LAYER 5 - L1 courses 2, 4, 6, 7
5 blanks, 13 pieces

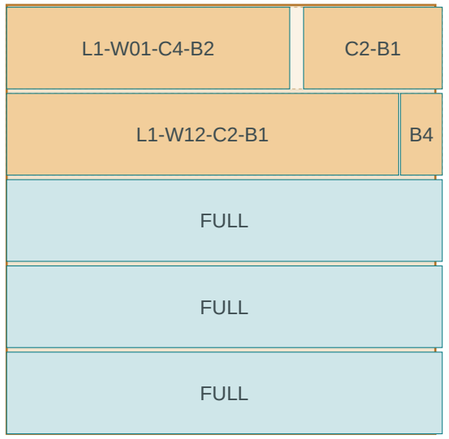


LAYER 4 - L1 courses 2, 4
5 blanks, 7 pieces

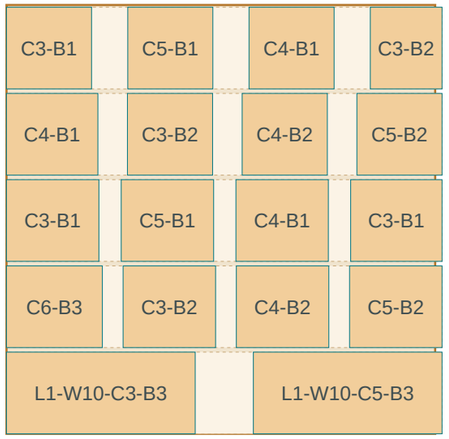


LAYER 3 - L1 courses 3-6
5 blanks, 18 pieces

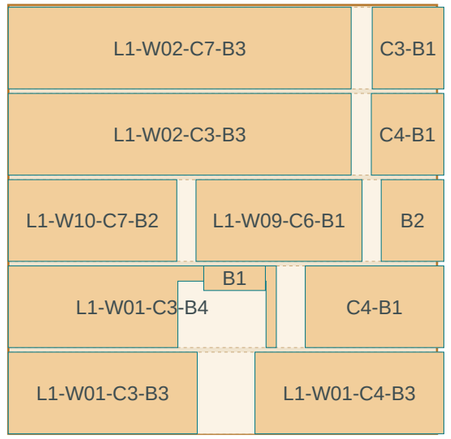

LAYER 2 - L1 courses 3, 4, 6, 7
5 blanks, 12 pieces

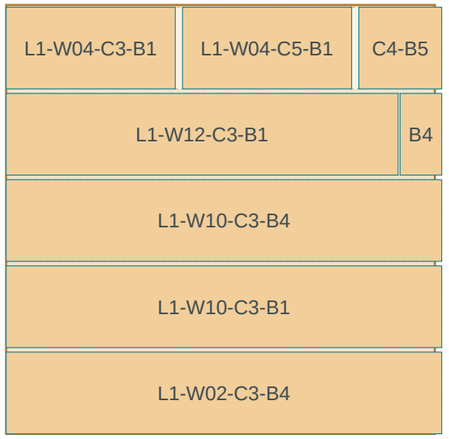

LAYER 1 - L1 courses 3-6
5 blanks, 8 pieces

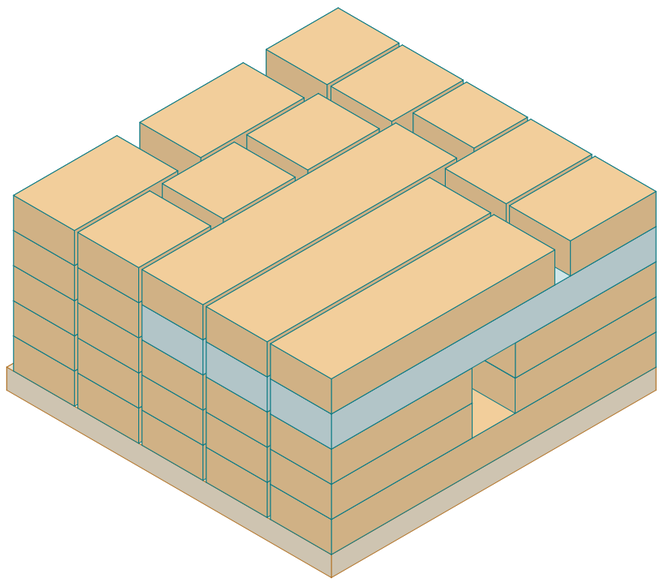

ISOMETRIC 5 layers, built bottom up

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L1 courses 3-6 (place first)
- ☐ L1-W02-C3-B4
- ☐ L1-W10-C3-B1
- ☐ L1-W10-C3-B4
- ☐ L1-W12-C3-B1
- ☐ L1-W10-C6-B4
- ☐ L1-W04-C3-B1
- ☐ L1-W04-C5-B1
- ☐ L1-W01-C4-B5

LAYER 2 - L1 courses 3, 4, 6, 7
- ☐ L1-W01-C3-B3
- ☐ L1-W01-C4-B3
- ☐ L1-W01-C3-B4
- ☐ L1-W03-C6-B1
- ☐ L1-W11-C4-B1
- ☐ L1-W10-C7-B2
- ☐ L1-W09-C6-B1
- ☐ L1-W02-C3-B2
- ☐ L1-W02-C3-B3
- ☐ L1-W10-C4-B1
- ☐ L1-W02-C7-B3
- ☐ L1-W07-C3-B1

LAYER 3 - L1 courses 3-6
- ☐ L1-W10-C3-B3
- ☐ L1-W10-C5-B3
- ☐ L1-W10-C6-B3
- ☐ L1-W06-C3-B2
- ☐ L1-W06-C4-B2
- ☐ L1-W06-C5-B2
- ☐ L1-W06-C3-B1
- ☐ L1-W06-C5-B1
- ☐ L1-W06-C4-B1
- ☐ L1-W01-C3-B1
- ☐ L1-W01-C4-B1
- ☐ L1-W07-C3-B2
- ☐ L1-W07-C4-B2
- ☐ L1-W07-C5-B2
- ☐ L1-W05-C3-B1
- ☐ L1-W05-C5-B1
- ☐ L1-W05-C4-B1
- ☐ L1-W05-C3-B2


LAYER 4 - L1 courses 2, 4
- ☐ FULL form
- ☐ FULL form
- ☐ FULL form
- ☐ L1-W12-C2-B1

LAYER 4 - L1 courses 2, 4 (continued)
- ☐ L1-W10-C4-B4
- ☐ L1-W01-C4-B2
- ☐ L1-W11-C2-B1


LAYER 5 - L1 courses 2, 4, 6, 7
- ☐ L1-W05-C2-B1
- ☐ L1-W08-C2-B2
- ☐ L1-W07-C2-B1
- ☐ L1-W08-C4-B2
- ☐ L1-W01-C2-B3
- ☐ L1-W07-C4-B1
- ☐ L1-W04-C4-B1
- ☐ L1-W04-C6-B1
- ☐ L1-W10-C2-B3
- ☐ L1-W10-C4-B3
- ☐ L1-W11-C6-B1
- ☐ L1-W11-C7-B1
- ☐ L1-W04-C2-B1

Checked by _____


Date _____




DETAIL A
layer 5, 2x



DETAIL C
layer 5, 2x



DETAIL B
layer 5, 2x



DETAIL D
layer 5, 2x

Pieces without a detail here: see the placement checklist (15)


Nudura™ **PALLET STACK SHEET** **CUT-3**

Plan view, top layer first - build from the bottom up


PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	5
SERIES	6in XR35	HEIGHT	1293 mm
FORMS	25	PALLET	2400 x 2400

Stack CUT-4 - 6in XR35 straights


25 blanks, 36 pieces | 5 layers | L1 courses 4-7 | stack height 1293 mm of 1300 mm cap

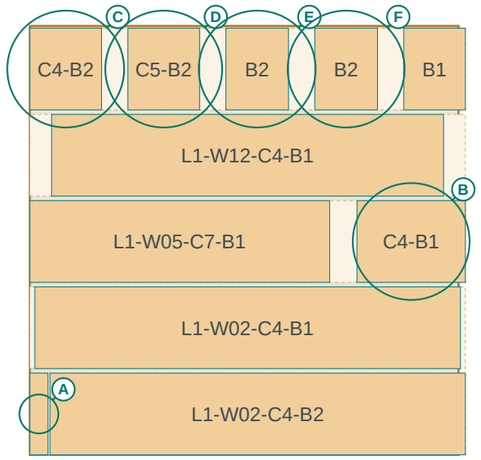


LAYER 5 - L1 courses 4, 5, 7
5 blanks, 11 pieces

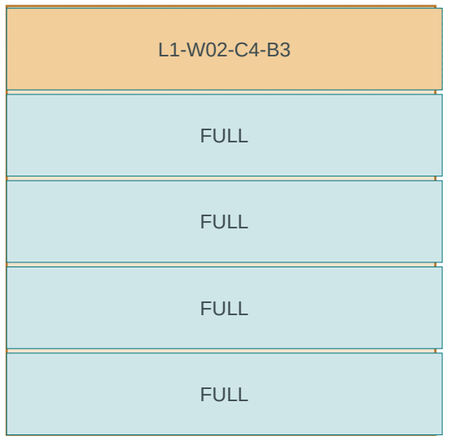


LAYER 4 - L1 course 4
5 blanks, 5 pieces

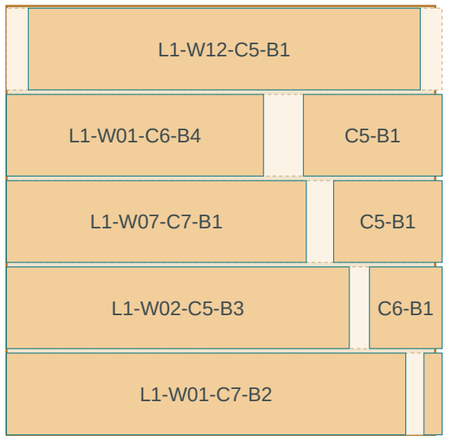


LAYER 3 - L1 courses 5-7
5 blanks, 9 pieces

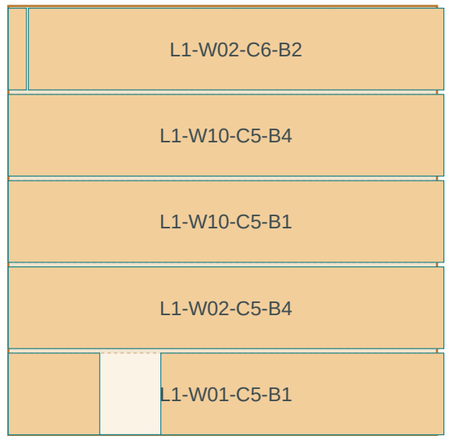

LAYER 2 - L1 courses 5-6
5 blanks, 6 pieces

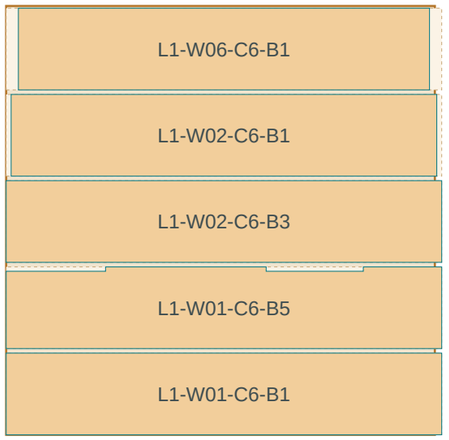

LAYER 1 - L1 course 6
5 blanks, 5 pieces

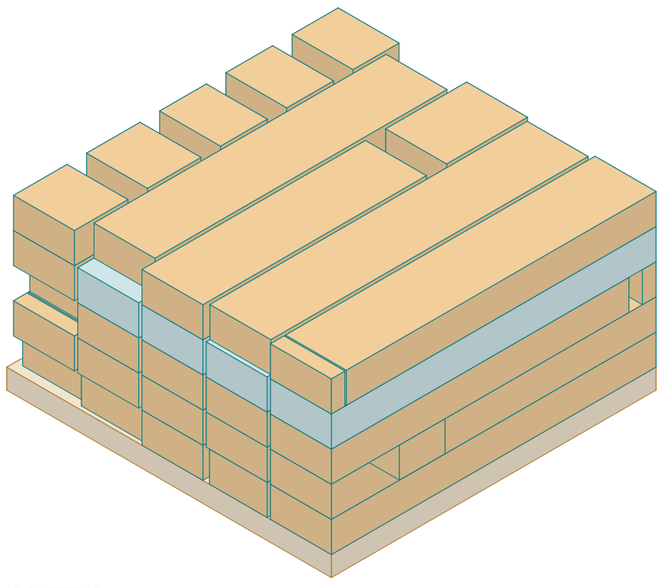

ISOMETRIC 5 layers, built bottom up

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L1 course 6 (place first)
- ☐ L1-W01-C6-B1
- ☐ L1-W01-C6-B5
- ☐ L1-W02-C6-B3
- ☐ L1-W02-C6-B1
- ☐ L1-W06-C6-B1

LAYER 2 - L1 courses 5-6
- ☐ L1-W01-C5-B1
- ☐ L1-W02-C5-B4
- ☐ L1-W10-C5-B1
- ☐ L1-W10-C5-B4
- ☐ L1-W01-C5-B2
- ☐ L1-W02-C6-B2


LAYER 3 - L1 courses 5-7
- ☐ L1-W01-C7-B2
- ☐ L1-W01-C5-B3
- ☐ L1-W02-C5-B3
- ☐ L1-W10-C6-B1
- ☐ L1-W07-C7-B1
- ☐ L1-W09-C5-B1
- ☐ L1-W01-C6-B4
- ☐ L1-W11-C5-B1
- ☐ L1-W12-C5-B1

LAYER 4 - L1 course 4
- ☐ FULL form
- ☐ FULL form
- ☐ FULL form
- ☐ FULL form
- ☐ L1-W02-C4-B3


LAYER 5 - L1 courses 4, 5, 7
- ☐ L1-W10-C4-B6
- ☐ L1-W02-C4-B2
- ☐ L1-W02-C4-B1
- ☐ L1-W05-C7-B1
- ☐ L1-W09-C4-B1
- ☐ L1-W12-C4-B1
- ☐ L1-W05-C4-B2
- ☐ L1-W05-C5-B2
- ☐ L1-W02-C5-B2
- ☐ L1-W02-C7-B2
- ☐ L1-W03-C7-B1

Checked by _____


Date _____




DETAIL A
layer 5, 6x




DETAIL C
layer 5, 2x




DETAIL E
layer 5, 2x



DETAIL B
layer 5, 2x



DETAIL D
layer 5, 2x



DETAIL F
layer 5, 2x

Pieces without a detail here: see the placement checklist (5)


Nudura™ **PALLET STACK SHEET** **CUT-4**

Plan view, top layer first - build from the bottom up


PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	5
SERIES	6in XR35	HEIGHT	1293 mm
FORMS	25	PALLET	2400 x 2400

Stack CUT-5 - 6in XR35 straights

19 blanks, 22 pieces | 4 layers | L1 courses 6-7 | stack height 1064 mm of 1300 mm cap

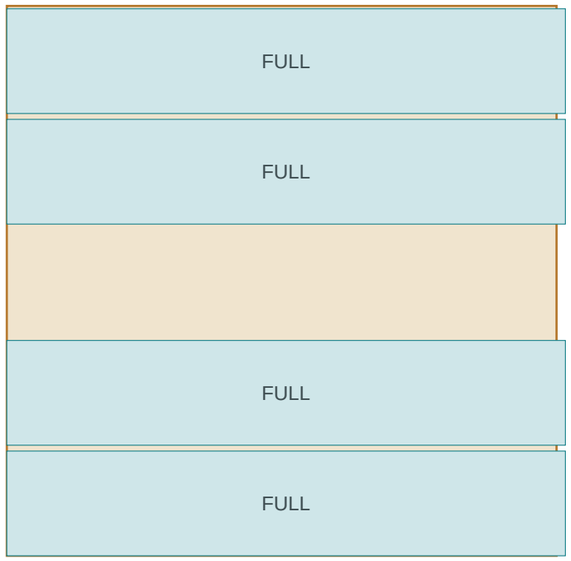


LAYER 4
4 blanks, 4 pieces

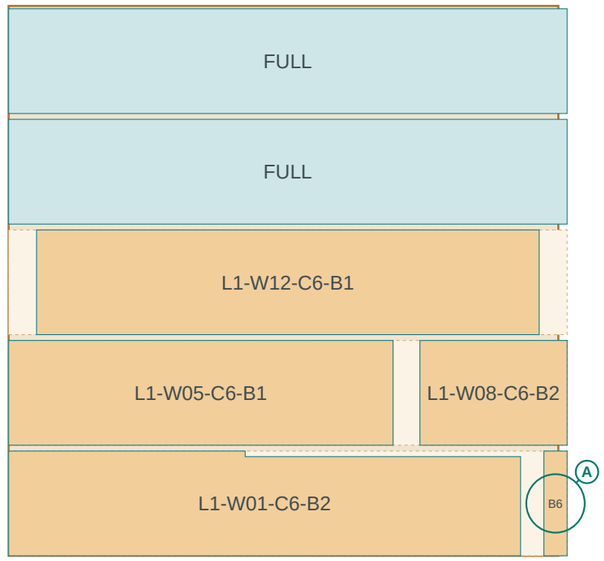


LAYER 3 - L1 course 6
5 blanks, 7 pieces



LAYER 2 - L1 course 7
5 blanks, 6 pieces

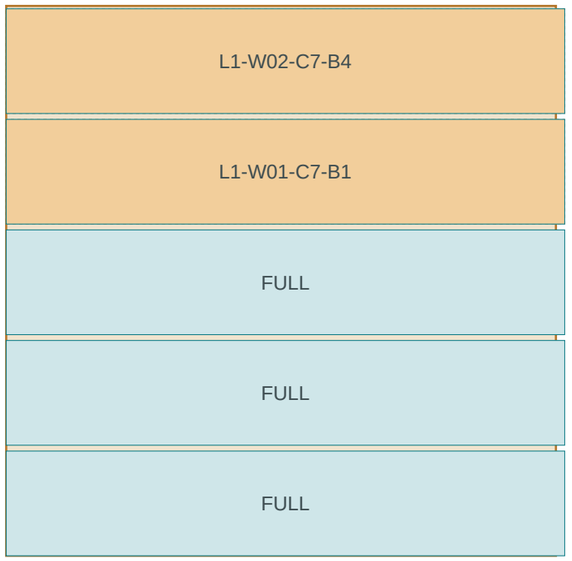

LAYER 1 - L1 course 7
5 blanks, 5 pieces

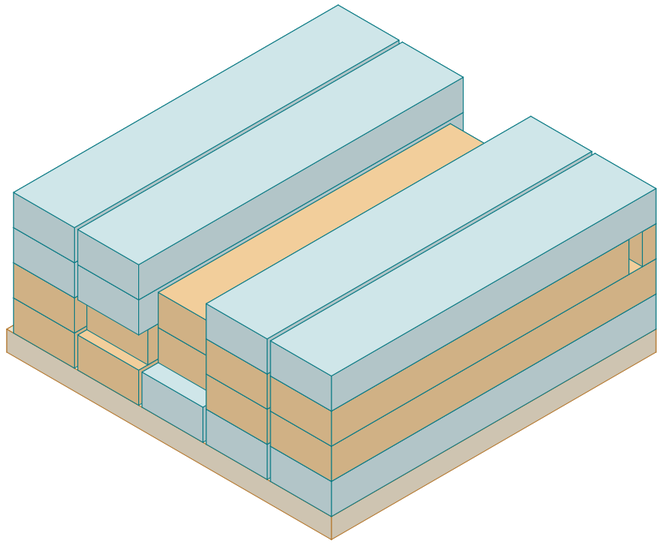

ISOMETRIC 4 layers, built bottom up

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L1 course 7 (place first)
- ☐ FULL form
- ☐ FULL form
- ☐ FULL form
- ☐ L1-W01-C7-B1
- ☐ L1-W02-C7-B4

LAYER 2 - L1 course 7
- ☐ L1-W10-C7-B1
- ☐ L1-W10-C7-B4
- ☐ L1-W12-C7-B1
- ☐ L1-W06-C7-B1
- ☐ L1-W10-C7-B3
- ☐ L1-W01-C7-B4

LAYER 3 - L1 course 6
- ☐ L1-W01-C6-B2
- ☐ L1-W10-C6-B6
- ☐ L1-W05-C6-B1
- ☐ L1-W08-C6-B2
- ☐ L1-W12-C6-B1
- ☐ FULL form
- ☐ FULL form

LAYER 4
- ☐ FULL form
- ☐ FULL form
- ☐ FULL form
- ☐ FULL form

Checked by _____

Date _____

DETAIL A
layer 3, 4x

Nudura™

PALLET STACK SHEET


CUT-5

Plan view, top layer first - build from the bottom up

PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	4
SERIES	6in XR35	HEIGHT	1064 mm
FORMS	19	PALLET	2400 x 2400

Stack CNR-3 - 6in XR35 corners

4 blanks, 4 pieces | 1 layers | L1 course 7 | stack height 607 mm of 1300 mm cap

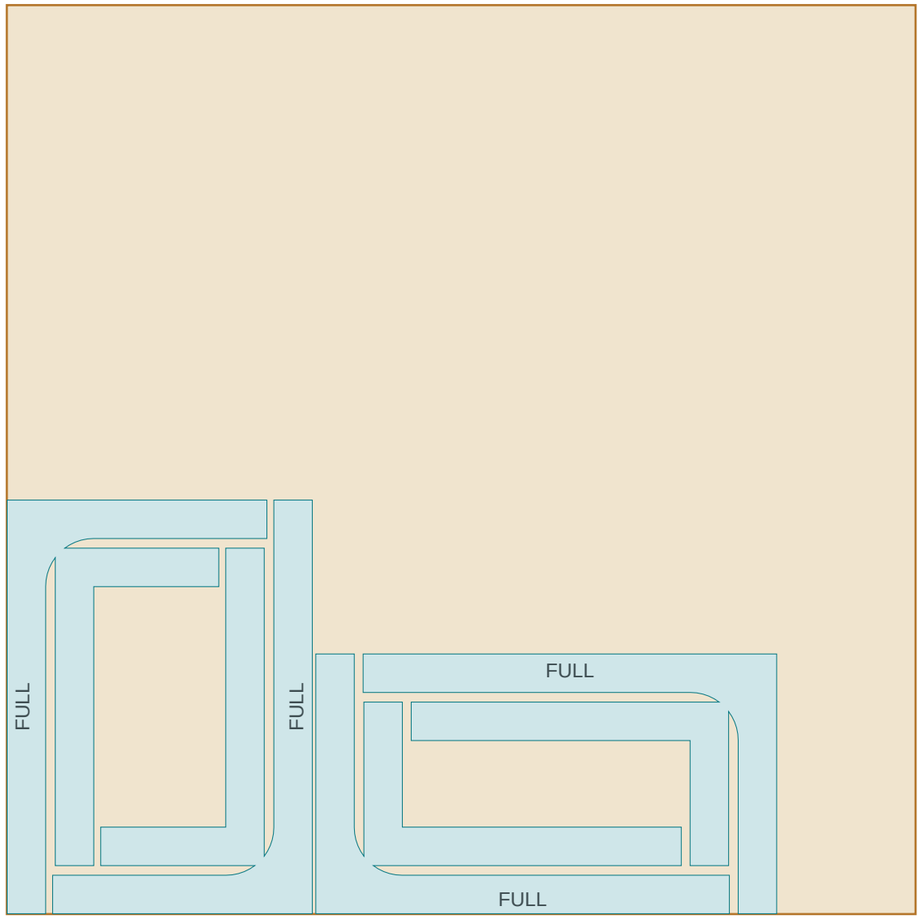

LAYER 1 - L1 course 7
4 blanks, 4 pieces


PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L1 course 7 (place first)

- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner

Checked by _____

Date _____

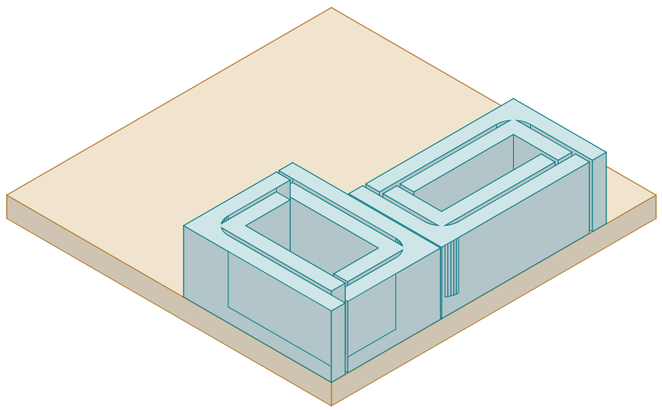

Nudura™

PALLET STACK SHEET


CNR-3

Plan view, top layer first - build from the bottom up


PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	1
SERIES	6in XR35	HEIGHT	607 mm
FORMS	4	PALLET	2400 x 2400

Stack CNR-4 - 6in XR35 corners


24 blanks, 24 pieces | 2 layers | L2 courses 1-3 | stack height 1064 mm of 1300 mm cap

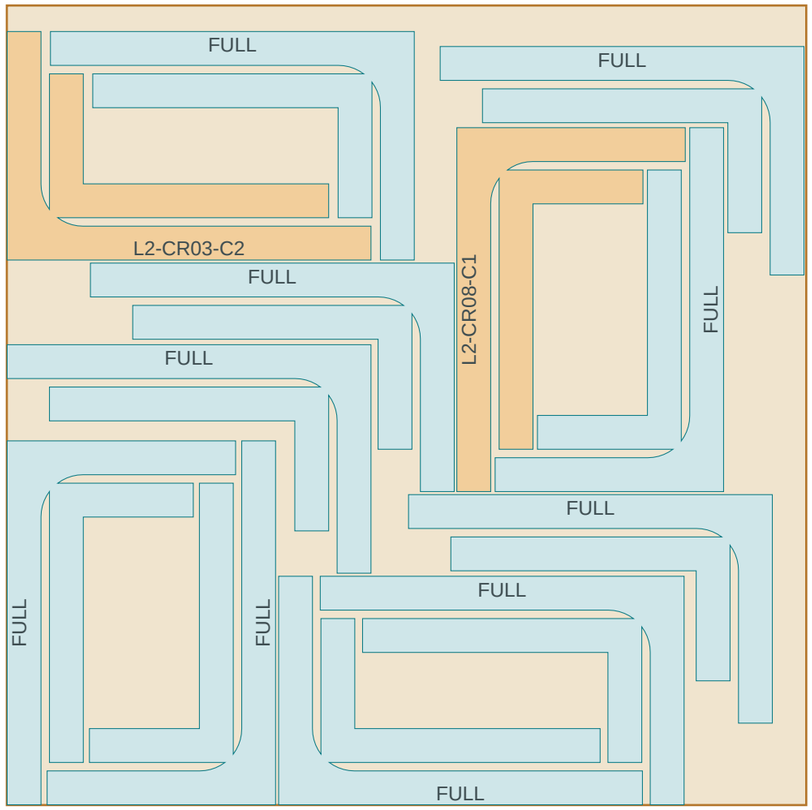

LAYER 2 - L2 courses 1-2
12 blanks, 12 pieces

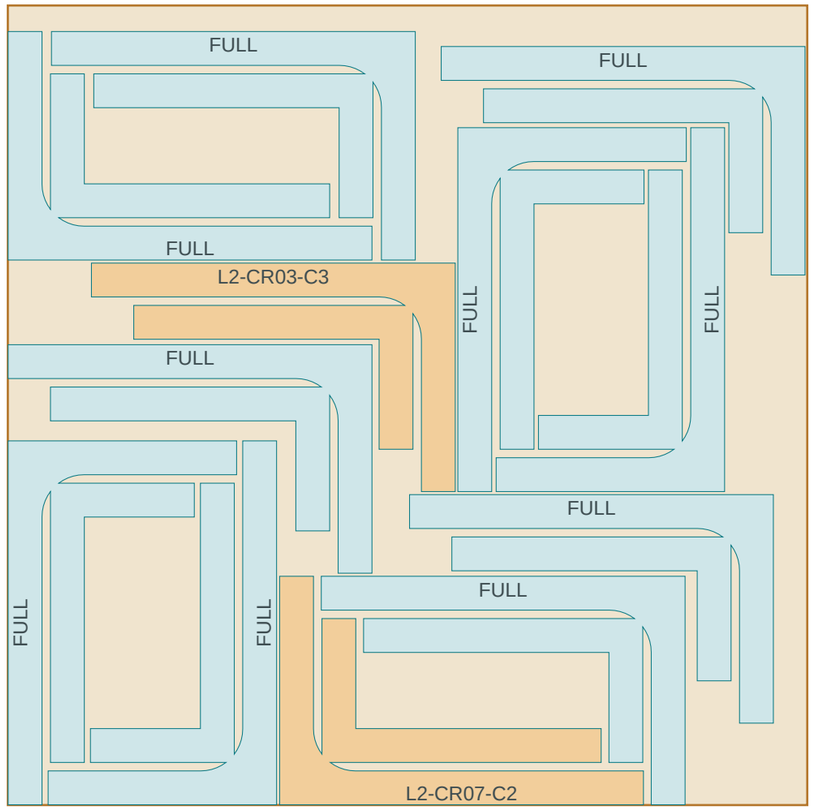

LAYER 1 - L2 courses 2-3
12 blanks, 12 pieces

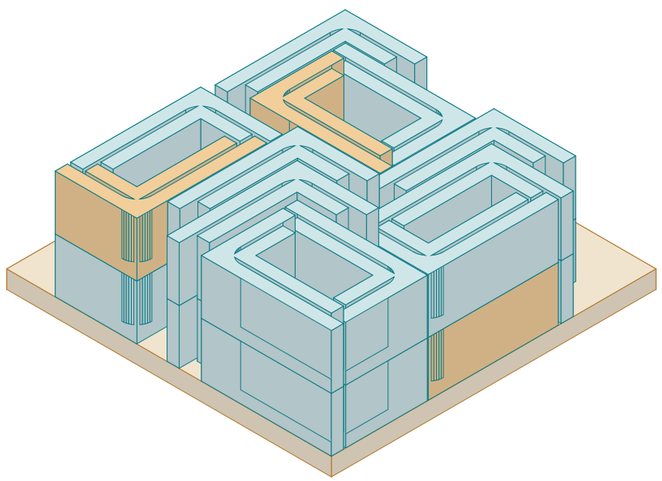

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L2 courses 2-3 (place first)

- ☐ FULL corner
- ☐ FULL corner
- ☐ L2-CR07-C2
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ L2-CR03-C3
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner

LAYER 2 - L2 courses 1-2

- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ L2-CR08-C1
- ☐ FULL corner
- ☐ FULL corner
- ☐ L2-CR03-C2

LAYER 2 - L2 courses 1-2 (continued)

- ☐ FULL corner

Checked by _____

Date _____

Nudura™

PALLET STACK SHEET


CNR-4

Plan view, top layer first - build from the bottom up


PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	2
SERIES	6in XR35	HEIGHT	1064 mm
FORMS	24	PALLET	2400 x 2400

Stack CUT-6 - 6in XR35 straights


25 blanks, 50 pieces | 5 layers | L2 courses 1-6 | stack height 1293 mm of 1300 mm cap

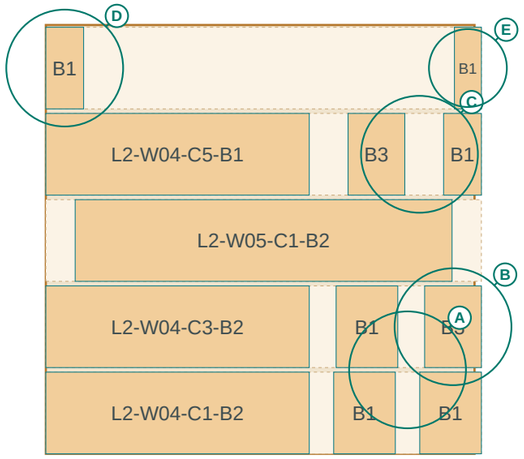


LAYER 5 - L2 courses 1-5
5 blanks, 12 pieces

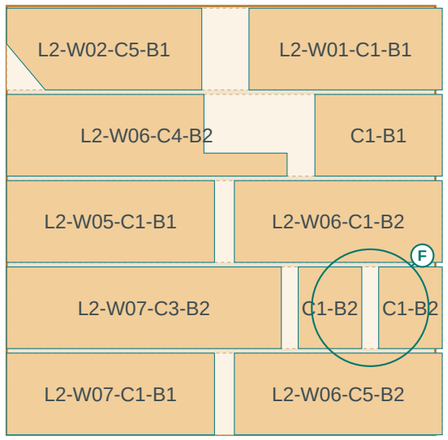


LAYER 4 - L2 courses 1, 3, 4, 5
5 blanks, 11 pieces

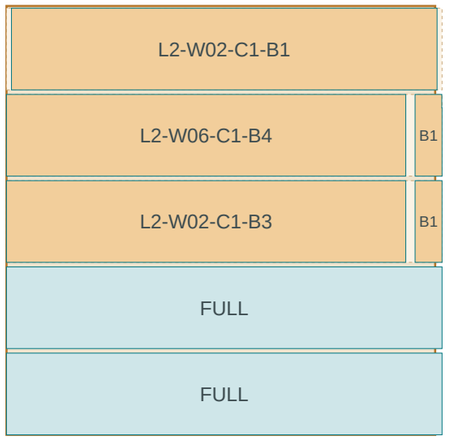


LAYER 3 - L2 courses 1-3
5 blanks, 7 pieces

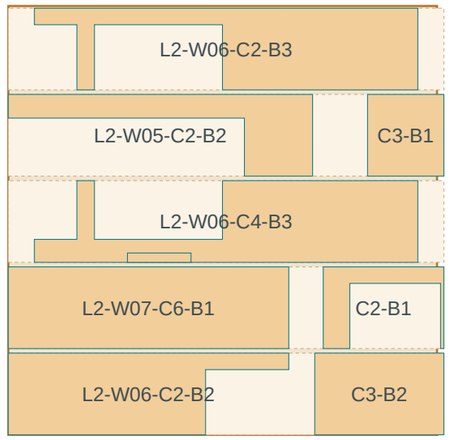

LAYER 2 - L2 courses 2, 3, 4, 6
5 blanks, 9 pieces

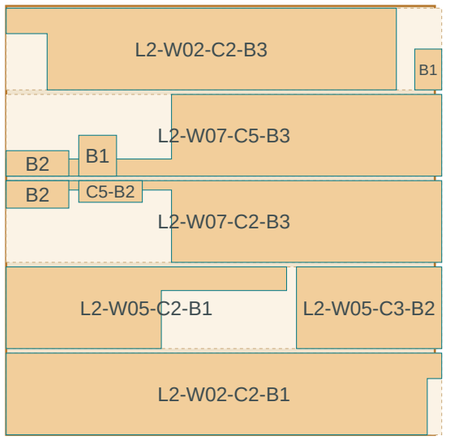

LAYER 1 - L2 courses 2-5
5 blanks, 11 pieces

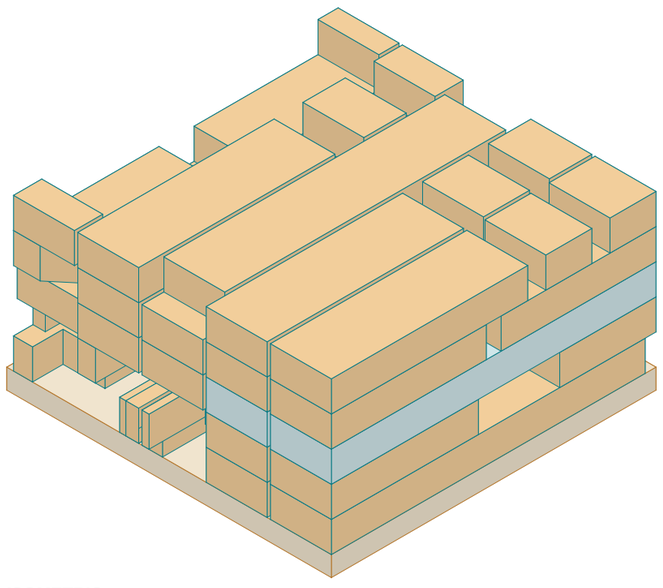

ISOMETRIC 5 layers, built bottom up

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L2 courses 2-5 (place first)
- ☐ L2-W02-C2-B1
- ☐ L2-W05-C2-B1
- ☐ L2-W05-C3-B2
- ☐ L2-W07-C2-B3
- ☐ L2-W02-C4-B2
- ☐ L2-W07-C5-B2
- ☐ L2-W07-C5-B3
- ☐ L2-W02-C2-B2
- ☐ L2-W09-C4-B1
- ☐ L2-W02-C2-B3
- ☐ L2-W10-C4-B1

LAYER 2 - L2 courses 2, 3, 4, 6
- ☐ L2-W06-C2-B2
- ☐ L2-W06-C3-B2
- ☐ L2-W07-C6-B1
- ☐ L2-W01-C2-B1
- ☐ L2-W06-C4-B3
- ☐ L2-W07-C2-B2
- ☐ L2-W05-C2-B2
- ☐ L2-W07-C3-B1
- ☐ L2-W06-C2-B3

LAYER 3 - L2 courses 1-3
- ☐ FULL form
- ☐ FULL form
- ☐ L2-W02-C1-B3
- ☐ L2-W08-C3-B1
- ☐ L2-W06-C1-B4
- ☐ L2-W10-C2-B1
- ☐ L2-W02-C1-B1


LAYER 4 - L2 courses 1, 3, 4, 5
- ☐ L2-W07-C1-B1
- ☐ L2-W06-C5-B2
- ☐ L2-W07-C3-B2
- ☐ L2-W02-C1-B2
- ☐ L2-W07-C1-B2
- ☐ L2-W05-C1-B1
- ☐ L2-W06-C1-B2
- ☐ L2-W06-C4-B2
- ☐ L2-W04-C1-B1
- ☐ L2-W02-C5-B1
- ☐ L2-W01-C1-B1

LAYER 5 - L2 courses 1-5
- ☐ L2-W04-C1-B2
- ☐ L2-W03-C1-B1

LAYER 5 - L2 courses 1-5 (continued)
- ☐ L2-W03-C2-B1
- ☐ L2-W04-C3-B2
- ☐ L2-W03-C4-B1
- ☐ L2-W06-C1-B3
- ☐ L2-W05-C1-B2
- ☐ L2-W04-C5-B1
- ☐ L2-W06-C5-B3
- ☐ L2-W09-C1-B1
- ☐ L2-W09-C3-B1
- ☐ L2-W08-C1-B1


Checked by _____

Date _____




DETAIL A
layer 5, 2x


DETAIL C
layer 5, 2x




DETAIL E
layer 5, 3x



DETAIL B
layer 5, 2x



DETAIL D
layer 5, 2x



DETAIL F
layer 4, 2x

Pieces without a detail here: see the placement checklist (8)

Nudura™

PALLET STACK SHEET


CUT-6

Plan view, top layer first - build from the bottom up


PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	5
SERIES	6in XR35	HEIGHT	1293 mm
FORMS	25	PALLET	2400 x 2400

Stack CUT-7 - 6in XR35 straights


25 blanks, 44 pieces | 5 layers | L2 courses 2-6 | stack height 1293 mm of 1300 mm cap

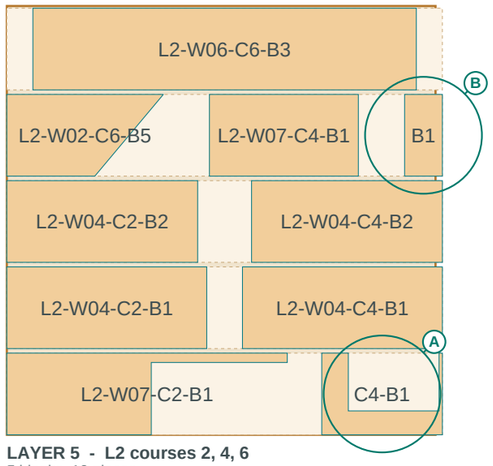


LAYER 5 - L2 courses 2, 4, 6
5 blanks, 10 pieces

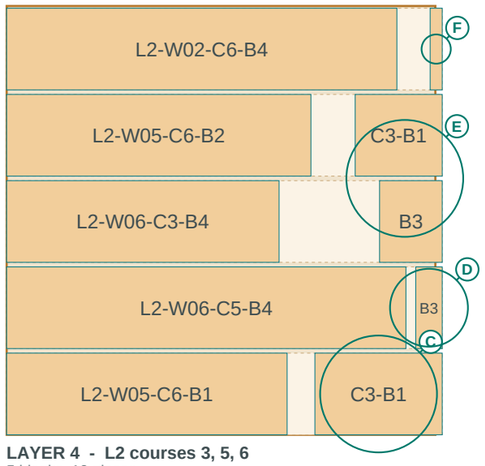


LAYER 4 - L2 courses 3, 5, 6
5 blanks, 10 pieces

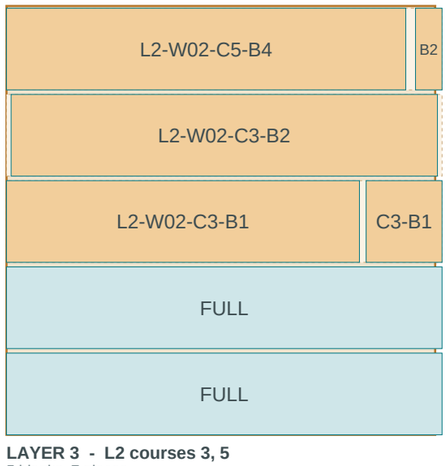


LAYER 3 - L2 courses 3, 5
5 blanks, 7 pieces

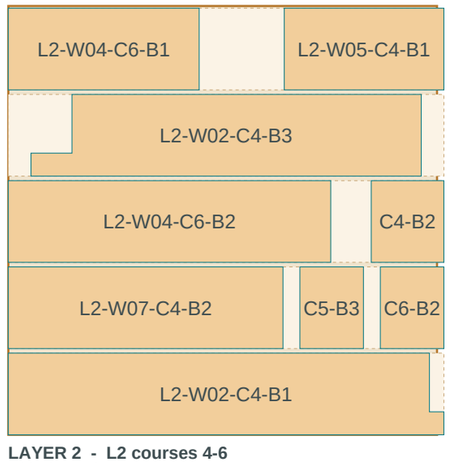

LAYER 2 - L2 courses 4-6
5 blanks, 9 pieces

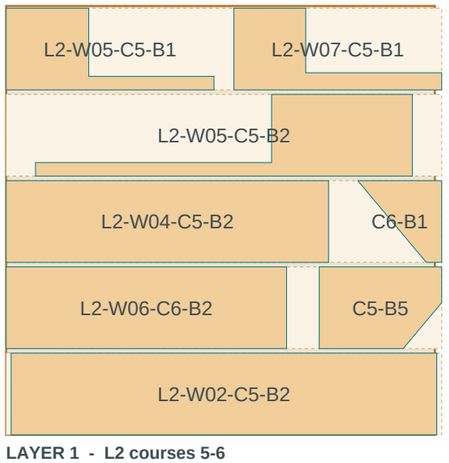

LAYER 1 - L2 courses 5-6
5 blanks, 8 pieces

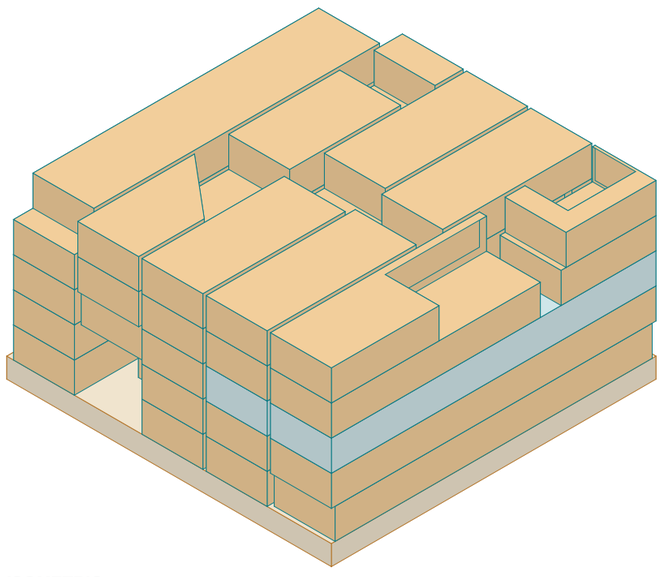

ISOMETRIC 5 layers, built bottom up

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L2 courses 5-6 (place first)
- ☐ L2-W02-C5-B2
- ☐ L2-W06-C6-B2
- ☐ L2-W02-C5-B5
- ☐ L2-W04-C5-B2
- ☐ L2-W02-C6-B1
- ☐ L2-W05-C5-B2
- ☐ L2-W05-C5-B1
- ☐ L2-W07-C5-B1

LAYER 2 - L2 courses 4-6
- ☐ L2-W02-C4-B1
- ☐ L2-W07-C4-B2
- ☐ L2-W02-C5-B3
- ☐ L2-W07-C6-B2
- ☐ L2-W04-C6-B2
- ☐ L2-W05-C4-B2
- ☐ L2-W02-C4-B3
- ☐ L2-W04-C6-B1
- ☐ L2-W05-C4-B1

LAYER 3 - L2 courses 3, 5
- ☐ FULL form
- ☐ FULL form
- ☐ L2-W02-C3-B1
- ☐ L2-W01-C3-B1
- ☐ L2-W02-C3-B2
- ☐ L2-W02-C5-B4
- ☐ L2-W01-C3-B2


LAYER 4 - L2 courses 3, 5, 6
- ☐ L2-W05-C6-B1
- ☐ L2-W04-C3-B1
- ☐ L2-W06-C5-B4
- ☐ L2-W06-C3-B3
- ☐ L2-W06-C3-B4
- ☐ L2-W02-C6-B3
- ☐ L2-W05-C6-B2
- ☐ L2-W05-C3-B1
- ☐ L2-W02-C6-B4
- ☐ L2-W03-C3-B1

LAYER 5 - L2 courses 2, 4, 6
- ☐ L2-W07-C2-B1
- ☐ L2-W01-C4-B1
- ☐ L2-W04-C2-B1
- ☐ L2-W04-C4-B1
- ☐ L2-W04-C2-B2
- ☐ L2-W04-C4-B2


LAYER 5 - L2 courses 2, 4, 6 (continued)
- ☐ L2-W02-C6-B5
- ☐ L2-W07-C4-B1
- ☐ L2-W09-C2-B1
- ☐ L2-W06-C6-B3

Checked by _____


Date _____




DETAIL A
layer 5, 2x




DETAIL C
layer 4, 2x




DETAIL E
layer 4, 2x



DETAIL B
layer 5, 2x



DETAIL D
layer 4, 3x



DETAIL F
layer 4, 8x

Pieces without a detail here: see the placement checklist (4)


Nudura™ **PALLET STACK SHEET** **CUT-7**

Plan view, top layer first - build from the bottom up


PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	5
SERIES	6in XR35	HEIGHT	1293 mm
FORMS	25	PALLET	2400 x 2400

Stack FULL-2 - 6in XR35 straights


11 blanks, 11 pieces | 3 layers | L2 courses 2-6 | stack height 836 mm of 1300 mm cap

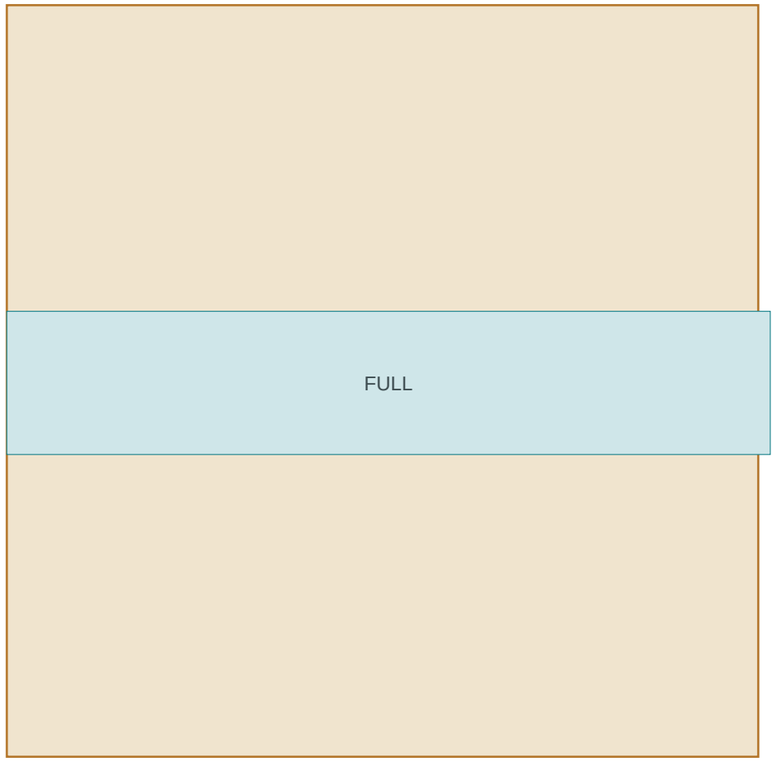

LAYER 3 - L2 course 6
1 blanks, 1 pieces

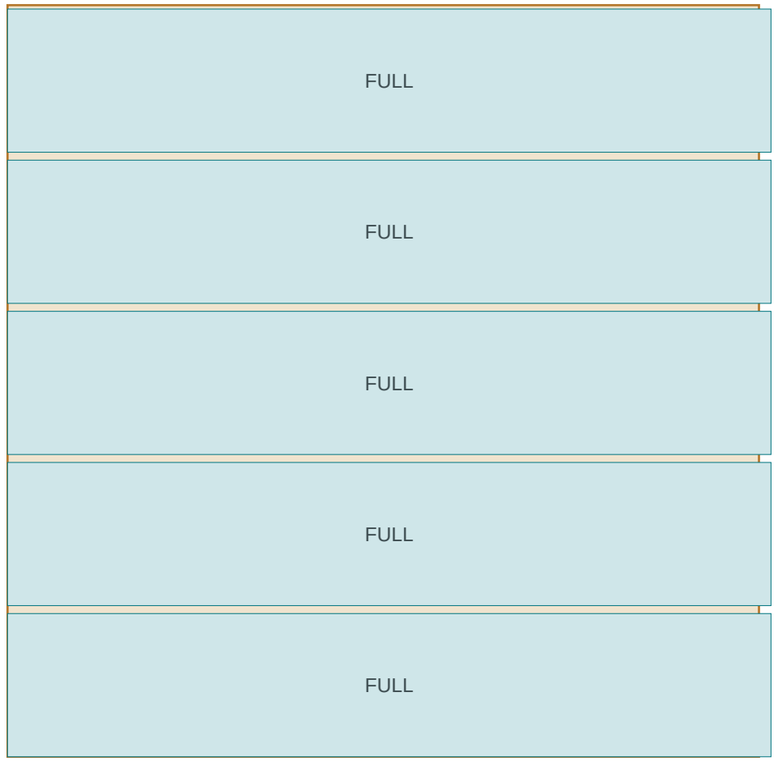

LAYER 2 - L2 courses 2-4
5 blanks, 5 pieces

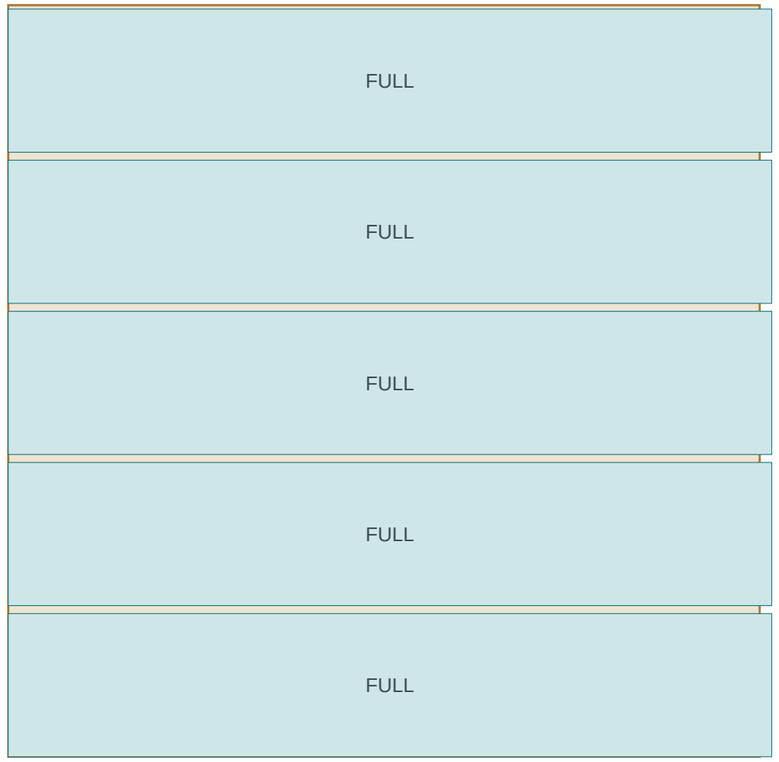

LAYER 1 - L2 courses 5-6
5 blanks, 5 pieces

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L2 courses 5-6 (place first)

- ☐ FULL form
- ☐ FULL form
- ☐ FULL form
- ☐ FULL form
- ☐ FULL form

LAYER 2 - L2 courses 2-4


- ☐ FULL form
- ☐ FULL form
- ☐ FULL form
- ☐ FULL form
- ☐ FULL form

LAYER 3 - L2 course 6

- ☐ FULL form

Checked by _____

Date _____

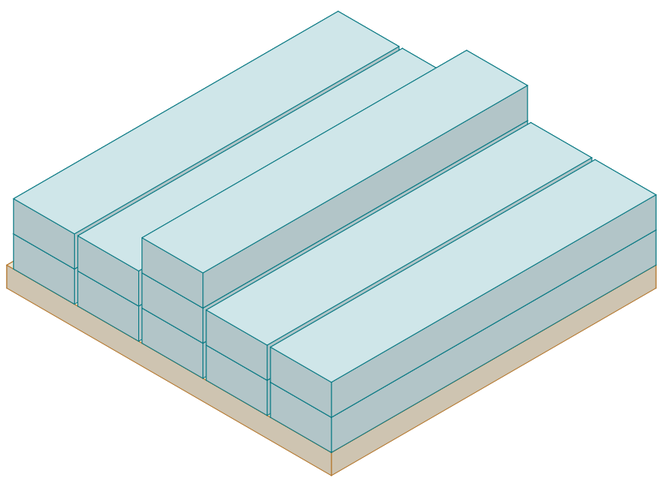

ISOMETRIC 3 layers, built bottom up

Nudura™

PALLET STACK SHEET


FULL-2

Plan view, top layer first - build from the bottom up


PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	3
SERIES	6in XR35	HEIGHT	836 mm
FORMS	11	PALLET	2400 x 2400

Stack CNR-5 - 6in XR35 corners


14 blanks, 14 pieces | 2 layers | L2 courses 4-6 | stack height 1064 mm of 1300 mm cap

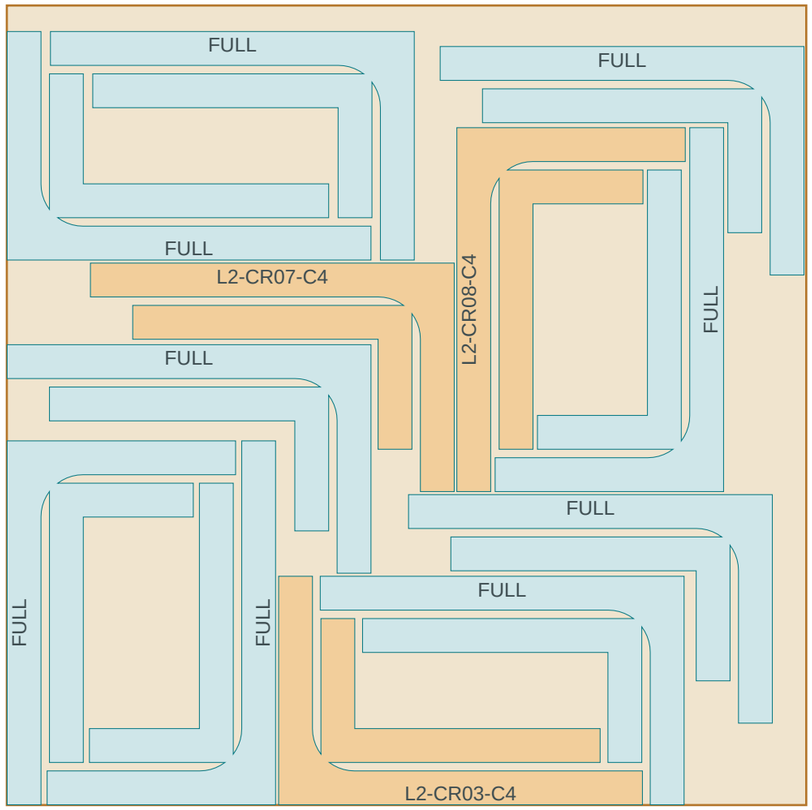

LAYER 2 - L2 courses 4-6
12 blanks, 12 pieces

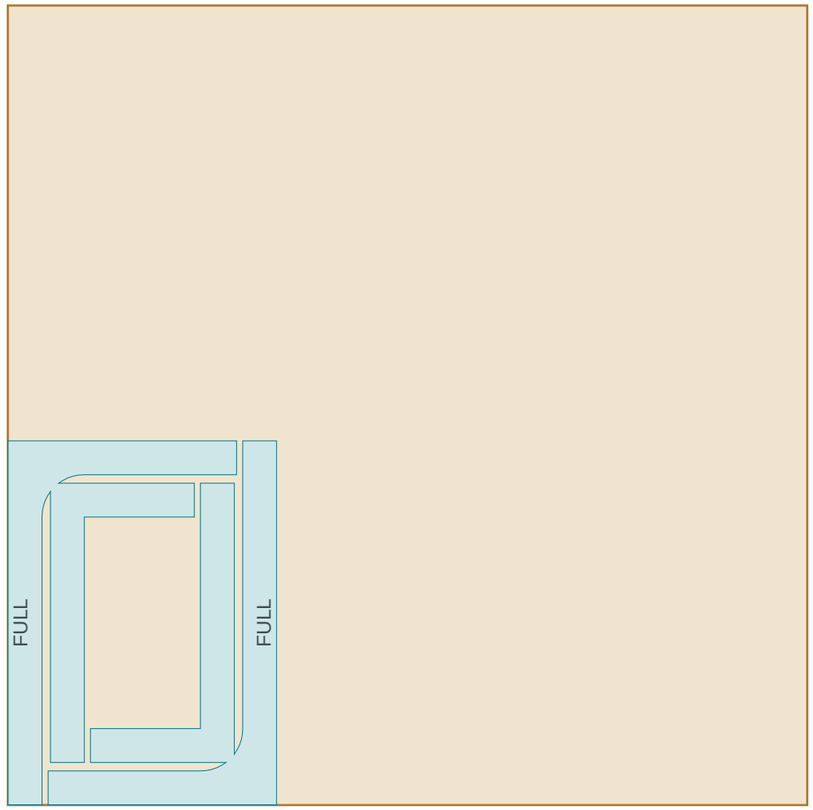

LAYER 1 - L2 course 6
2 blanks, 2 pieces

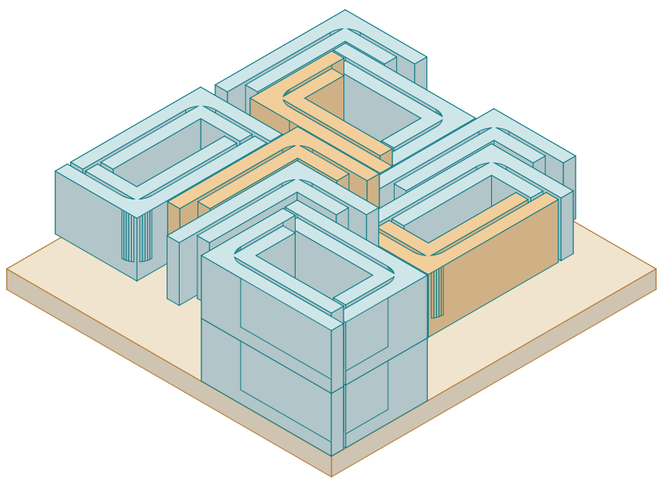

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L2 course 6 (place first)

- ☐ FULL corner
- ☐ FULL corner

LAYER 2 - L2 courses 4-6

- ☐ FULL corner
- ☐ FULL corner
- ☐ L2-CR03-C4
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ L2-CR07-C4
- ☐ L2-CR08-C4
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner

Checked by _____

Date _____

Nudura™

PALLET STACK SHEET


CNR-5

Plan view, top layer first - build from the bottom up

PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	**LAYERS**	2
SERIES	6in XR35	**HEIGHT**	1064 mm
FORMS	14	**PALLET**	2400 x 2400


Stack CNR-6 - 6in XR35 corners

14 blanks, 14 pieces | 2 layers | L3 courses 1-3 | stack height 1064 mm of 1300 mm cap

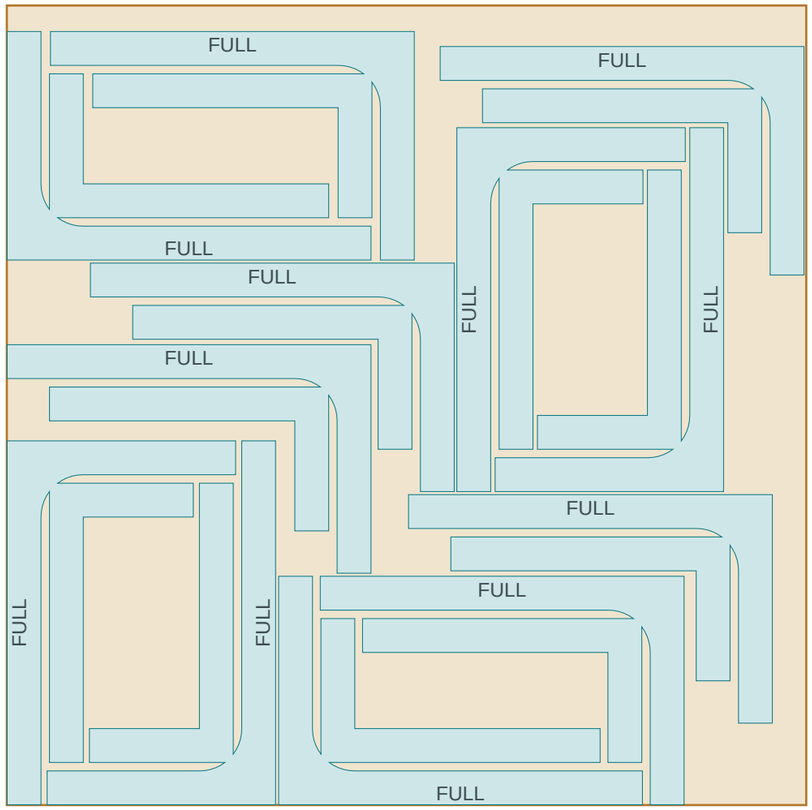


LAYER 2 - L3 courses 1-2

12 blanks, 12 pieces

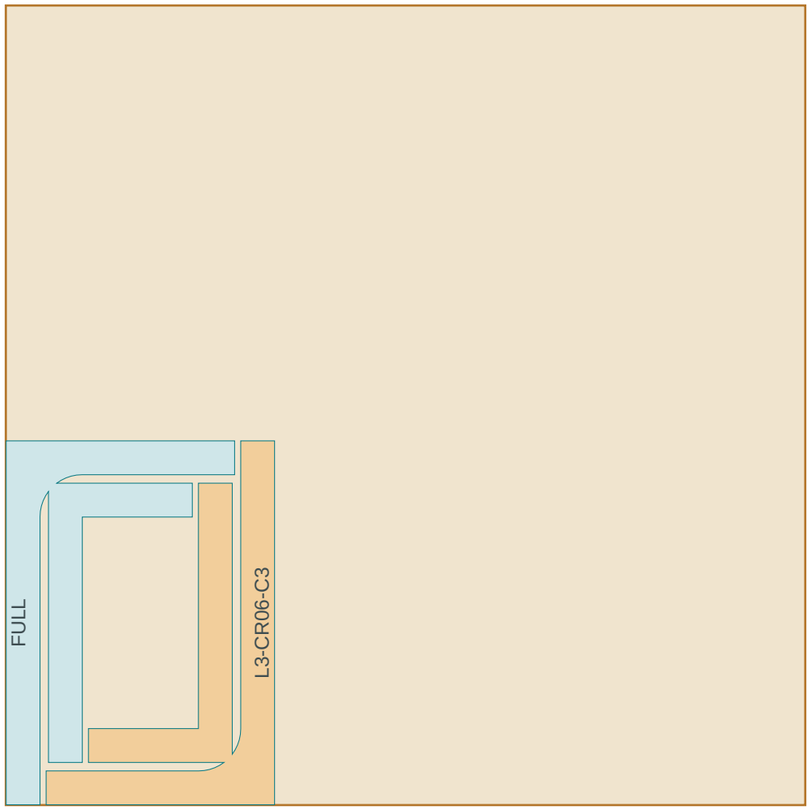

LAYER 1 - L3 course 3

2 blanks, 2 pieces

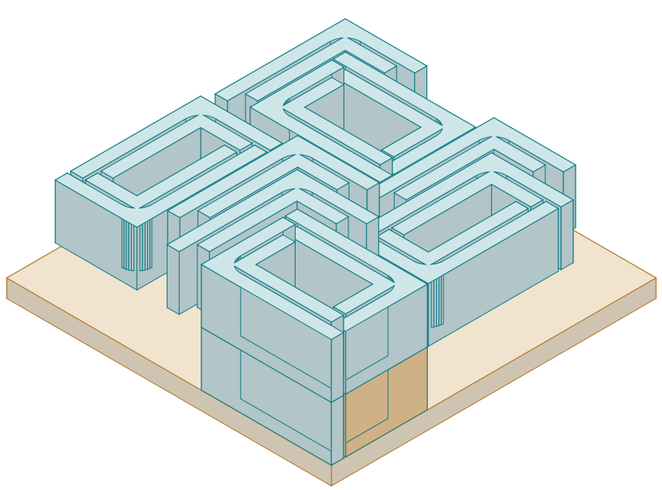

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L3 course 3 (place first)

- ☐ FULL corner
- ☐ L3-CR06-C3

LAYER 2 - L3 courses 1-2

- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner
- ☐ FULL corner

Checked by _____

Date _____

Nudura™

PALLET STACK SHEET


CNR-6

Plan view, top layer first - build from the bottom up


PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	**LAYERS**	2
SERIES	6in XR35	**HEIGHT**	1064 mm
FORMS	14	**PALLET**	2400 x 2400

Stack CUT-8 - 6in XR35 straights


25 blanks, 43 pieces | 5 layers | L3 courses 1, 2, 3, 5, 6, 7, 8, 9 | stack height 1293 mm of 1300 mm cap

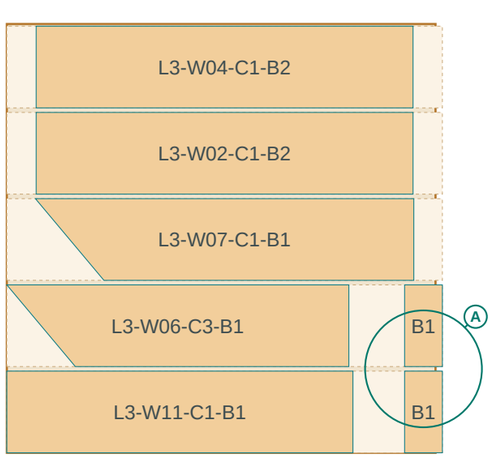


LAYER 5 - L3 courses 1-3
5 blanks, 7 pieces

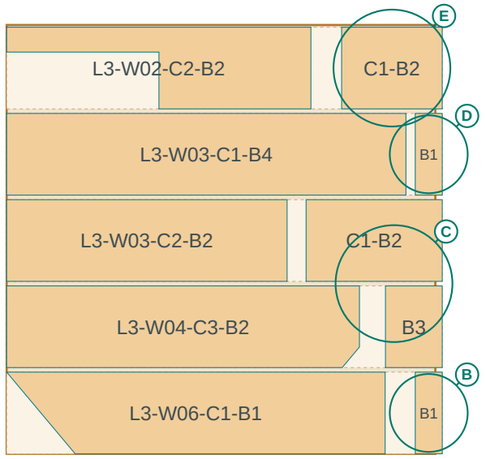


LAYER 4 - L3 courses 1-3
5 blanks, 10 pieces

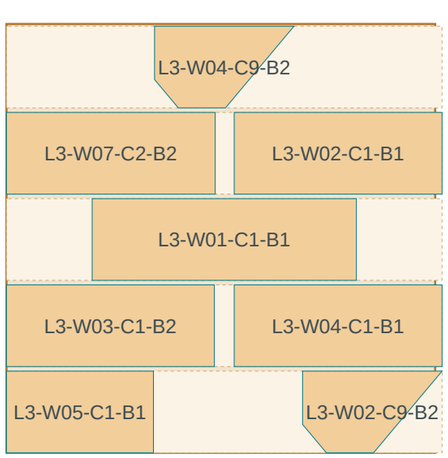

LAYER 3 - L3 courses 1, 2, 9
5 blanks, 8 pieces

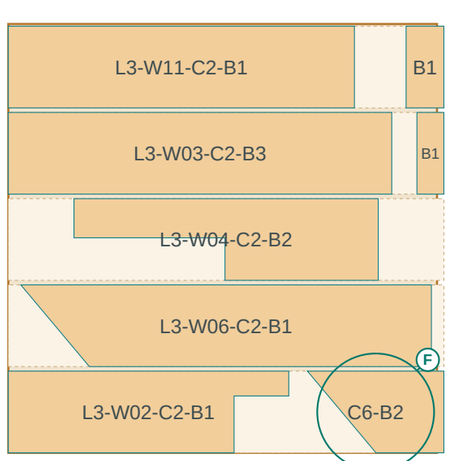


LAYER 2 - L3 courses 2, 3, 6
5 blanks, 8 pieces

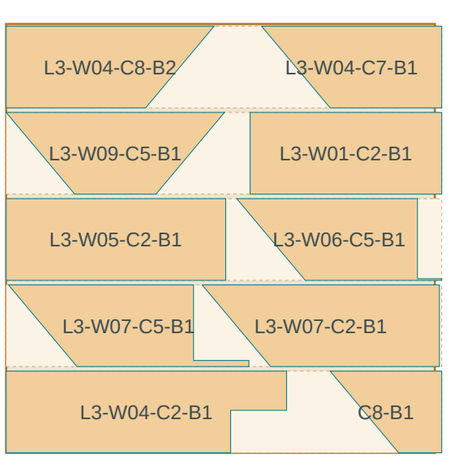

LAYER 1 - L3 courses 2, 5, 7, 8
5 blanks, 10 pieces

PACK UNDER BEFORE STACKING ON: L3-W03-C2-B2, L3-W07-C1-B2 overhangs 480 mm unsupported; L3-W03-C2-B2, L3-W07-C1-B2 overhangs 480 mm unsupported; L3-W02-C2-B2, L3-W06-C1-B2 overhangs 829 mm unsupported ...

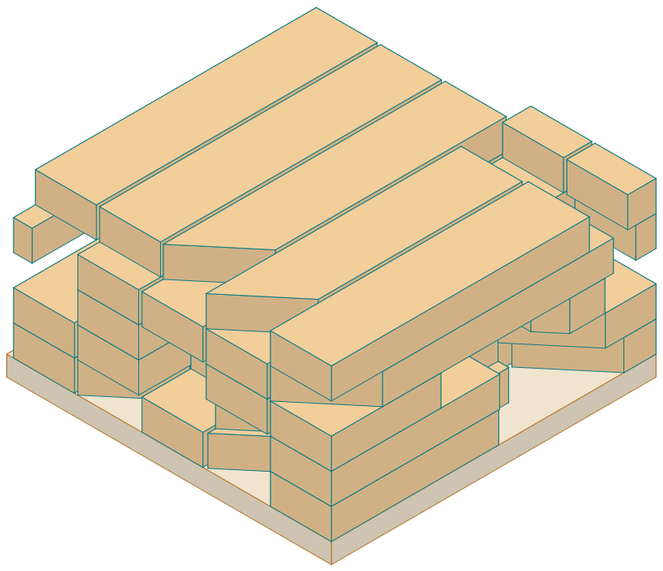

ISOMETRIC 5 layers, built bottom up

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L3 courses 2, 5, 7, 8 (place first)
- ☐ L3-W04-C2-B1
- ☐ L3-W04-C8-B1
- ☐ L3-W07-C5-B1
- ☐ L3-W07-C2-B1
- ☐ L3-W05-C2-B1
- ☐ L3-W06-C5-B1
- ☐ L3-W09-C5-B1
- ☐ L3-W01-C2-B1
- ☐ L3-W04-C8-B2
- ☐ L3-W04-C7-B1

LAYER 2 - L3 courses 2, 3, 6
- ☐ L3-W02-C2-B1
- ☐ L3-W06-C6-B2
- ☐ L3-W06-C2-B1
- ☐ L3-W04-C2-B2
- ☐ L3-W03-C2-B3
- ☐ L3-W10-C2-B1
- ☐ L3-W11-C2-B1
- ☐ L3-W09-C3-B1

LAYER 3 - L3 courses 1, 2, 9
- ☐ L3-W05-C1-B1
- ☐ L3-W02-C9-B2
- ☐ L3-W03-C1-B2
- ☐ L3-W04-C1-B1
- ☐ L3-W01-C1-B1
- ☐ L3-W07-C2-B2
- ☐ L3-W02-C1-B1
- ☐ L3-W04-C9-B2


LAYER 4 - L3 courses 1-3
- ☐ L3-W06-C1-B1
- ☐ L3-W08-C3-B1
- ☐ L3-W04-C3-B2
- ☐ L3-W03-C1-B3
- ☐ L3-W03-C2-B2
- ☐ L3-W07-C1-B2
- ☐ L3-W03-C1-B4
- ☐ L3-W08-C1-B1
- ☐ L3-W02-C2-B2
- ☐ L3-W06-C1-B2

LAYER 5 - L3 courses 1-3
- ☐ L3-W11-C1-B1
- ☐ L3-W09-C2-B1
- ☐ L3-W06-C3-B1
- ☐ L3-W09-C1-B1


LAYER 5 - L3 courses 1-3 (continued)
- ☐ L3-W07-C1-B1
- ☐ L3-W02-C1-B2
- ☐ L3-W04-C1-B2

Checked by _____


Date _____




DETAIL A
layer 5, 2x




DETAIL C
layer 4, 2x




DETAIL E
layer 4, 2x



DETAIL B
layer 4, 3x



DETAIL D
layer 4, 3x



DETAIL F
layer 2, 2x

Pieces without a detail here: see the placement checklist (3)


Nudura™ **PALLET STACK SHEET** **CUT-8**

Plan view, top layer first - build from the bottom up

PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	5
SERIES	6in XR35	HEIGHT	1293 mm
FORMS	25	PALLET	2400 x 2400

Stack FULL-3 - 6in XR35 straights

1 blanks, 1 pieces | 1 layers | L3 course 2 | stack height 379 mm of 1300 mm cap



LAYER 1 - L3 course 2

1 blanks, 1 pieces


PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L3 course 2 (place first)

- ☐ FULL form

Checked by _____

Date _____

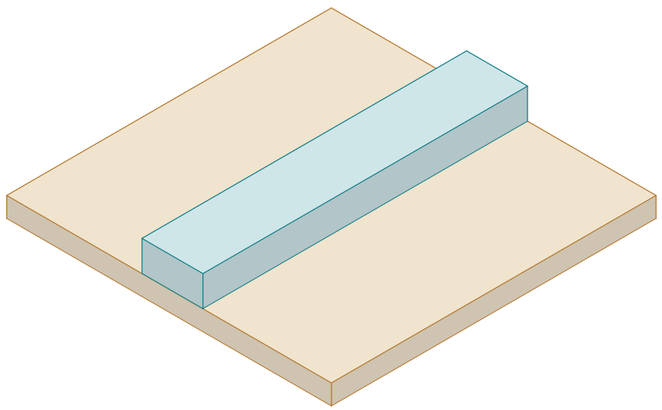


Nudura™ **PALLET STACK SHEET** **FULL-3**

Plan view, top layer first - build from the bottom up


PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	1
SERIES	6in XR35	HEIGHT	379 mm
FORMS	1	PALLET	2400 x 2400

Stack CUT-9 - 6in XR35 straights


25 blanks, 36 pieces | 5 layers | L3 courses 3-10 | stack height 1293 mm of 1300 mm cap

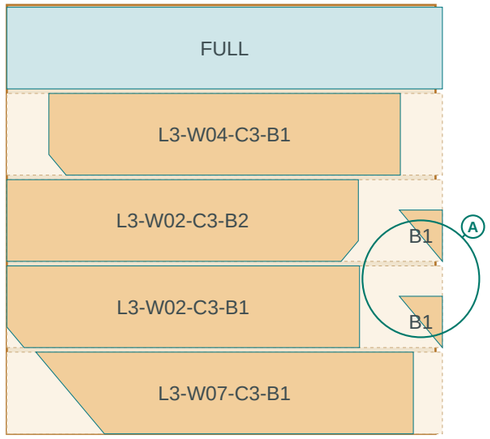


LAYER 5 - L3 courses 3, 9
5 blanks, 7 pieces

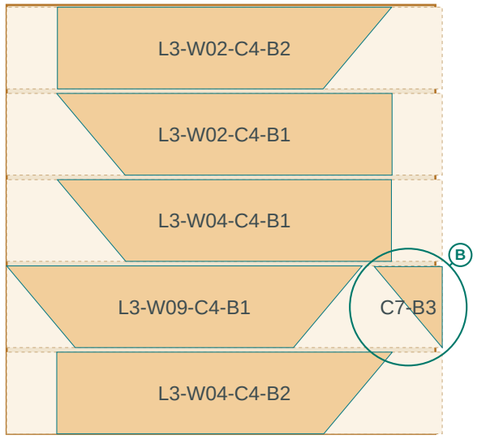


LAYER 4 - L3 courses 4, 7
5 blanks, 6 pieces

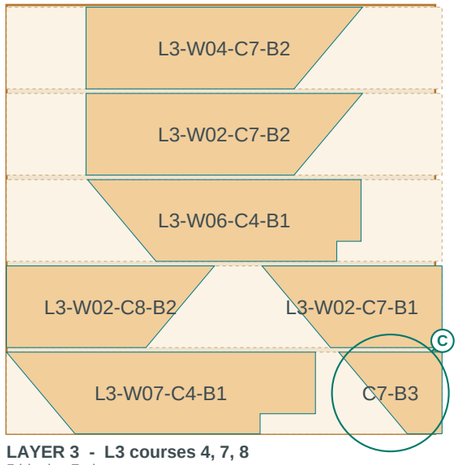

LAYER 3 - L3 courses 4, 7, 8
5 blanks, 7 pieces

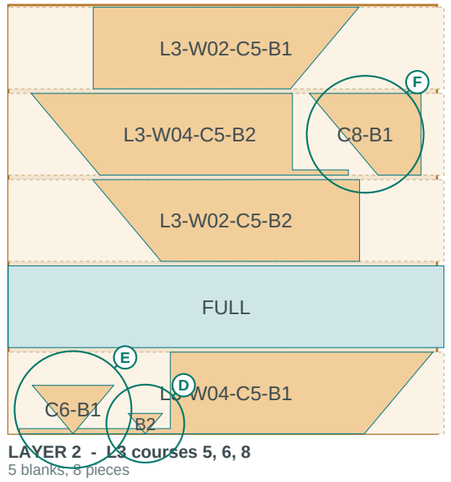


LAYER 2 - L3 courses 5, 6, 8
5 blanks, 8 pieces

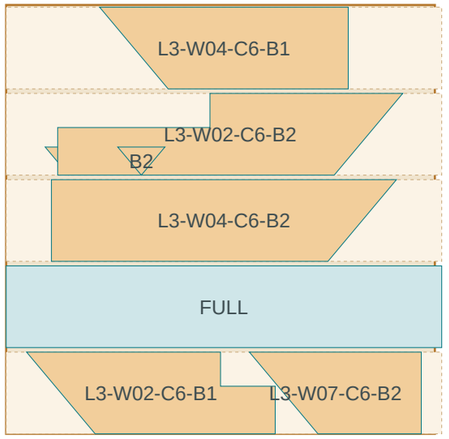

LAYER 1 - L3 courses 6, 10
5 blanks, 8 pieces

PACK UNDER BEFORE STACKING ON: L3-W02-C3-B2, L3-W04-C9-B1 has nothing under it

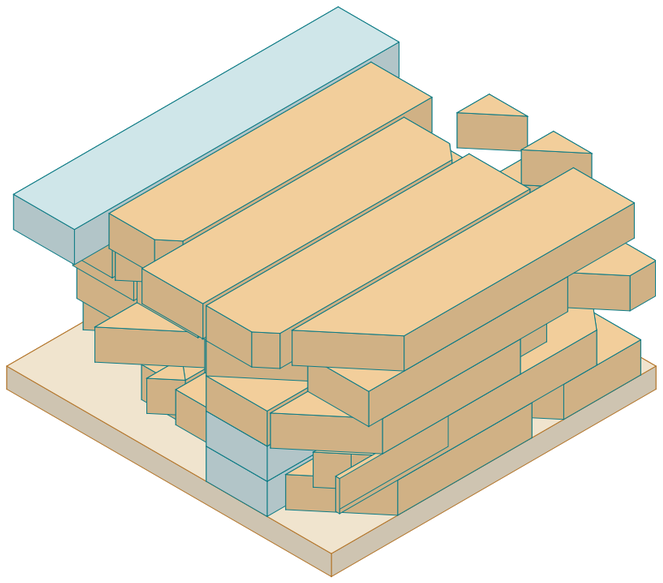

ISOMETRIC 5 layers, built bottom up

PLACEMENT CHECKLIST tick each form as it is placed - bottom layer first

LAYER 1 - L3 courses 6, 10 (place first)
- ☐ L3-W02-C6-B1
- ☐ L3-W07-C6-B2
- ☐ FULL form
- ☐ L3-W04-C6-B2
- ☐ L3-W02-C10-B2
- ☐ L3-W02-C6-B2
- ☐ L3-W04-C10-B2
- ☐ L3-W04-C6-B1

LAYER 2 - L3 courses 5, 6, 8
- ☐ L3-W04-C5-B1
- ☐ L3-W09-C6-B1
- ☐ L3-W07-C8-B2
- ☐ FULL form
- ☐ L3-W02-C5-B2
- ☐ L3-W04-C5-B2
- ☐ L3-W02-C8-B1
- ☐ L3-W02-C5-B1


LAYER 3 - L3 courses 4, 7, 8
- ☐ L3-W07-C4-B1
- ☐ L3-W07-C7-B3
- ☐ L3-W02-C8-B2
- ☐ L3-W02-C7-B1
- ☐ L3-W06-C4-B1
- ☐ L3-W02-C7-B2
- ☐ L3-W04-C7-B2

LAYER 4 - L3 courses 4, 7
- ☐ L3-W04-C4-B2
- ☐ L3-W09-C4-B1
- ☐ L3-W06-C7-B3
- ☐ L3-W04-C4-B1
- ☐ L3-W02-C4-B1
- ☐ L3-W02-C4-B2


LAYER 5 - L3 courses 3, 9
- ☐ L3-W07-C3-B1
- ☐ L3-W02-C3-B1
- ☐ L3-W02-C9-B1
- ☐ L3-W02-C3-B2
- ☐ L3-W04-C9-B1
- ☐ L3-W04-C3-B1
- ☐ FULL form

Checked by _____


Date _____




DETAIL A
layer 5, 2x




DETAIL C
layer 3, 2x




DETAIL E
layer 2, 2x



DETAIL B
layer 4, 2x



DETAIL D
layer 2, 3x



DETAIL F
layer 2, 2x

Pieces without a detail here: see the placement checklist (1)

Nudura™ **PALLET STACK SHEET** **CUT-9**

Plan view, top layer first - build from the bottom up

PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	LAYERS	5
SERIES	6in XR35	HEIGHT	1293 mm
FORMS	25	PALLET	2400 x 2400
