
SUPPLY SCOPE: Nudura ICF forms, accessories, pre-cut service, alignment hire and haulage as the quotation only. ENGLAND - Building Regulations. Ridge ~10.1 m, below 11 m. Floors, steels, stairs, roofs, windows and timber partitions are shown in good faith for coordination only - engineer / specialists to design.

QUOTATION - NOT FOR CONSTRUCTION

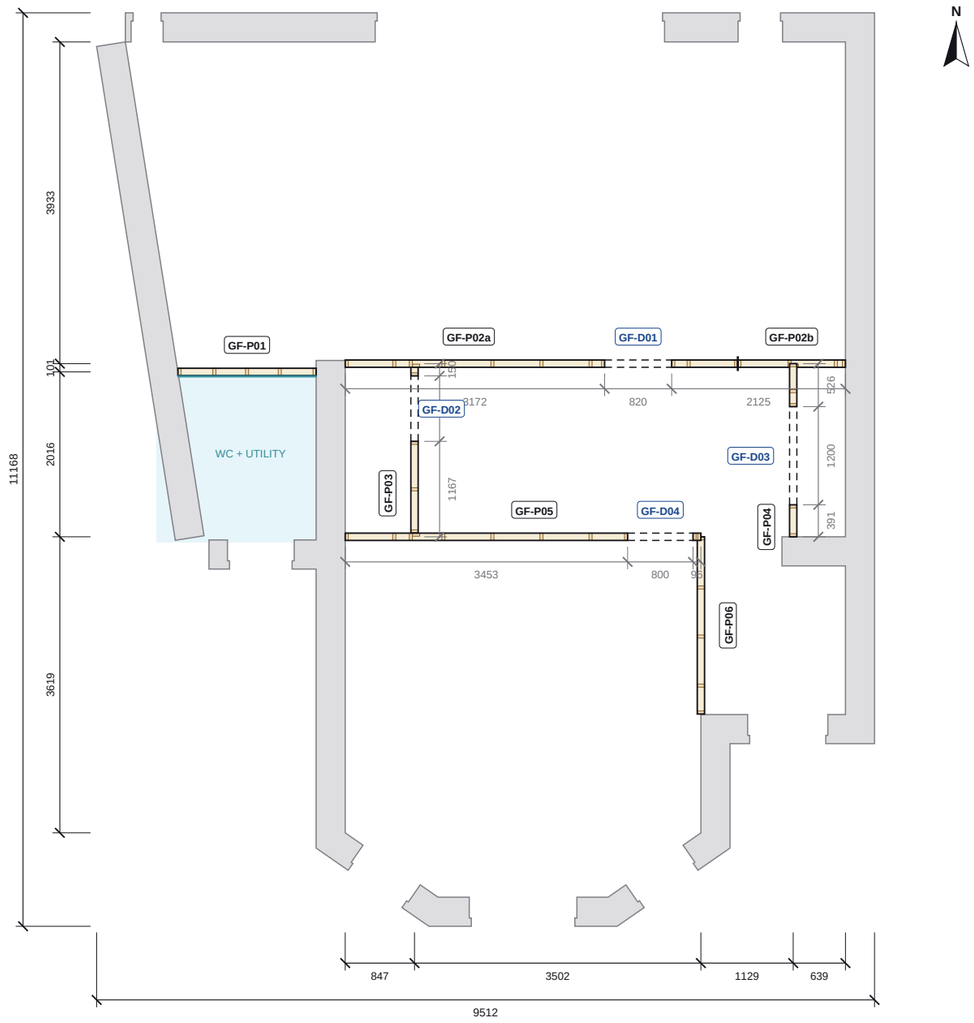

SOUTH (front, Clifton Park Road)

GROUND FLOOR TIMBER PARTITIONS PLAN

Scale 1:75 @ A3 | plan cut at 1,200 above GF FFL

0 1 2 3 4 5m

Partition panel 38x89 C16
Stud cut at plan level
Panel joint
Door opening, head over
18 WBP pattress (wet face)
Wet room
Nudura ICF (context only)

GROUND FLOOR SCHEDULES

PARTITION SCHEDULE

Wall	Panels	Length	Studs	Use	Head	Doors
GF-P01	IN1	1,690	38x89 C16 @400	wet room	2,725	-
GF-P02	IN3/IN4	6,117	38x89 C16 @600	partition	2,820	GF-D01
GF-P03	IN1	2,117	38x89 C16 @600	partition	2,820	GF-D02
GF-P04	IN6	2,117	38x89 C16 @600	partition	2,820	GF-D03
GF-P05	IN2	4,350	38x89 C16 @600	partition	2,820	GF-D04
GF-P06	IN5	2,167	38x89 C16 @600	partition	2,820	-
		18,558				**4 doors**

Panels = TLSTF panel names (IN..). Head = top of frame above GF FFL (z 0). Length along the wall (mm).

DOOR OPENING SCHEDULE

Door	Wall	Width	Height	Lvs	Note
GF-D01	GF-P02	820	2,100	1	hall -> dine / kitchen
GF-D02	GF-P03	800	2,100	1	hall -> WC + utility
GF-D03	GF-P04	1,200	2,100	2	cupboard bifold pair
GF-D04	GF-P05	800	2,100	1	hall -> sitting room

Structural opening sizes. Height = underside of the head rail above FFL.

PARTITION TIMBER (GF)

Member	Pieces	Run m
38x89 C16 studs (incl. king / junction)	61	139.6
38x89 C16 rails (head, sole, door head)	22	37.0
38x89 C16 noggins	34	13.2
Total 38x89 C16 (4.8 m lengths)	**42**	**189.9**

From the model (TLSTF members). 4.8 m lengths = run x 1.05 / 4.8, not cut-optimised.

HEAD CLIPS, NOGGINS, PATTRESS

Wall	Clips	Nogg.	Runs vs joists over
GF-P02	12	0	under a joist chord
GF-P03	5	0	across the joists
GF-P04	6	0	across the joists
GF-P05	3	3	parallel - noggins between
GF-P06	7	0	across the joists
Pattress 18 WBP	8		GF-P01 8

NOTES

1. Non-load-bearing partitions (TLSTF): 38x89 C16 studs @600 (@400 wet-room walls), rails + noggins, 15 plasterboard each side, insulation in the bays. By others - coordination only.
2. Heads stop 5 short of the 1F PS10 joist underside (+2,825; frame top +2,820), fixed with galv slotted deflection head clips to the joist bottom chords (33 No.) and 38x89 noggins between the chords where a partition runs parallel (3 No.) - clip product to CONFIRM. Floor over on ES26-065-FL-02.
3. Base = GF FFL +0: sole plates fixed down at <= 600 c/c to the screed / slab (DPC under). Set-out to partition centre lines; check on site.
4. Wet rooms (WC + utility): 18 WBP ply pattress in the stud bays on the wet-room face, 150-1,950 above the floor (8 pieces) for sanitaryware / wall-hung fixings.

REVISIONS

REV	DATE	DESCRIPTION
-	02.11.26	Quotation issue

Nudura™ BuildEase

CLIENT	PROJECT
Cuckfield Real Estate Ltd	Clifton College Garage Site, Clifton Park Road, Bristol

DRAWING TITLE

GROUND FLOOR TIMBER PARTITIONS

Internal stud partitions, panels and door openings

SCALE	SIZE	DATE
AS SHOWN	A3	02.11.26
DRAWN	**CHECKED**	**APPROVED**
TS		

STATUS	DRAWING No.	REV
QUOTATION	**ES26-065-TF-01**	-

Do not scale. All dimensions in mm. Check all dimensions on site.
