Delivery 1 - Load 1 of 1 - Artic 13.6 m

9 pallets in 4 of 5 floor positions | 161 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

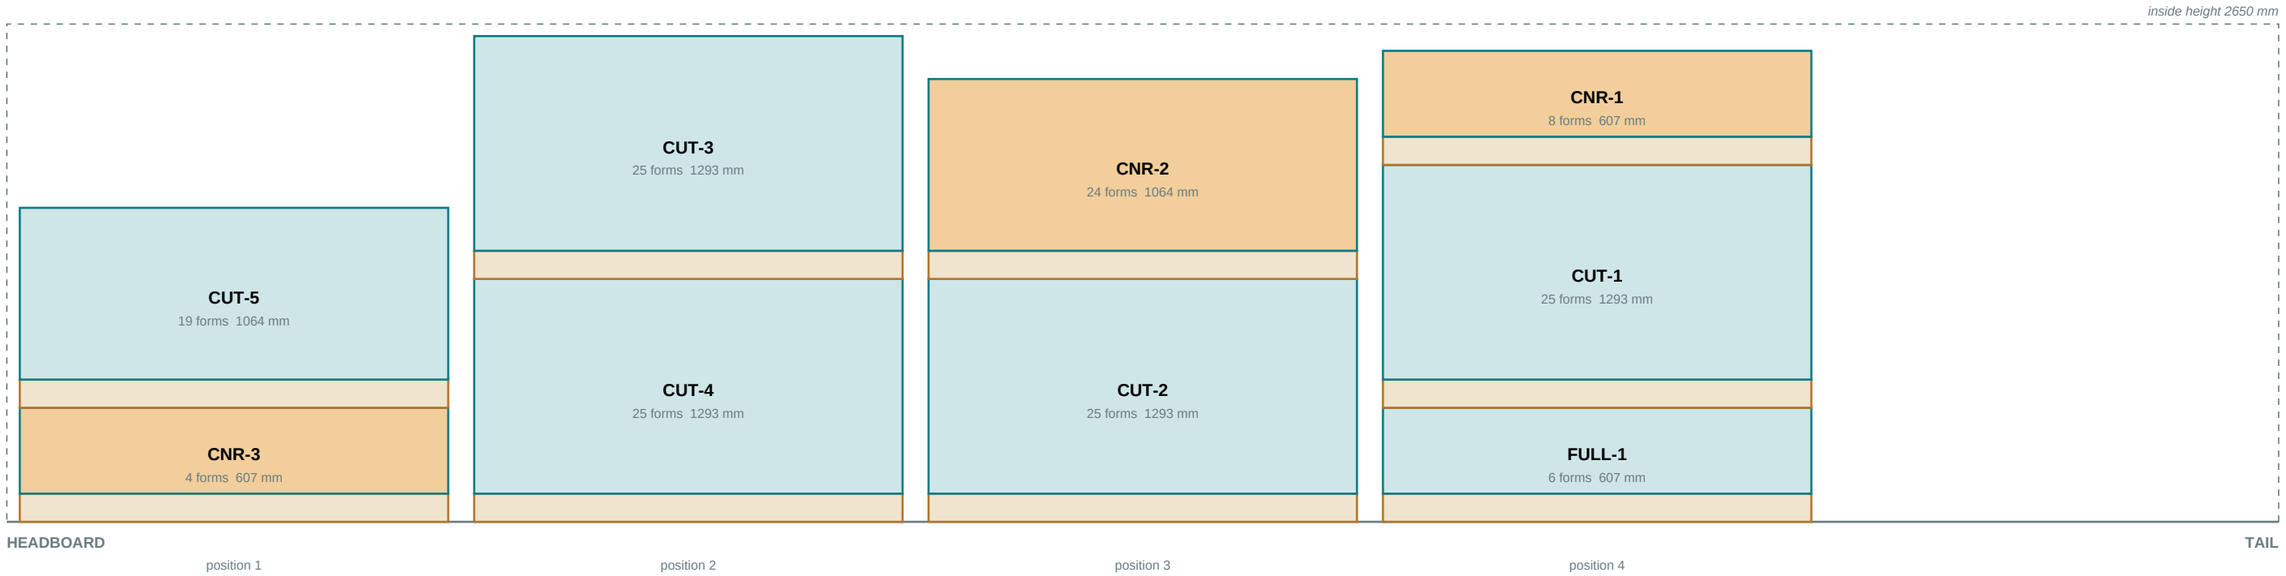

Unload order - 8 of 8 pallets come off out of build order, the price of stacking tallest forward

1. CNR-1 6in XR35 corners 8 forms courses FB courses 1-2
2. CUT-1 6in XR35 straights 25 forms courses FB courses 1-2
3. FULL-1 6in XR35 straights 6 forms courses FB courses 1-2
4. CNR-2 6in XR35 corners 24 forms courses L1 courses 1-6
5. CUT-2 6in XR35 straights 25 forms courses L1 courses 1-7
6. CUT-3 6in XR35 straights 25 forms courses L1 courses 2-7
7. CUT-4 6in XR35 straights 25 forms courses L1 courses 4-7
8. CUT-5 6in XR35 straights 19 forms courses L1 courses 6-7
9. CNR-3 6in XR35 corners 4 forms courses L1 course 7

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	FORMS	161
VEHICLE	Artic 13.6 m	POSITIONS	4 of 5
PALLETS	9	TALLEST	2586 mm

Delivery 2 - Load 1 of 1 - Artic 13.6 m

9 pallets in 5 of 5 floor positions | 164 forms | tallest column 2357 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

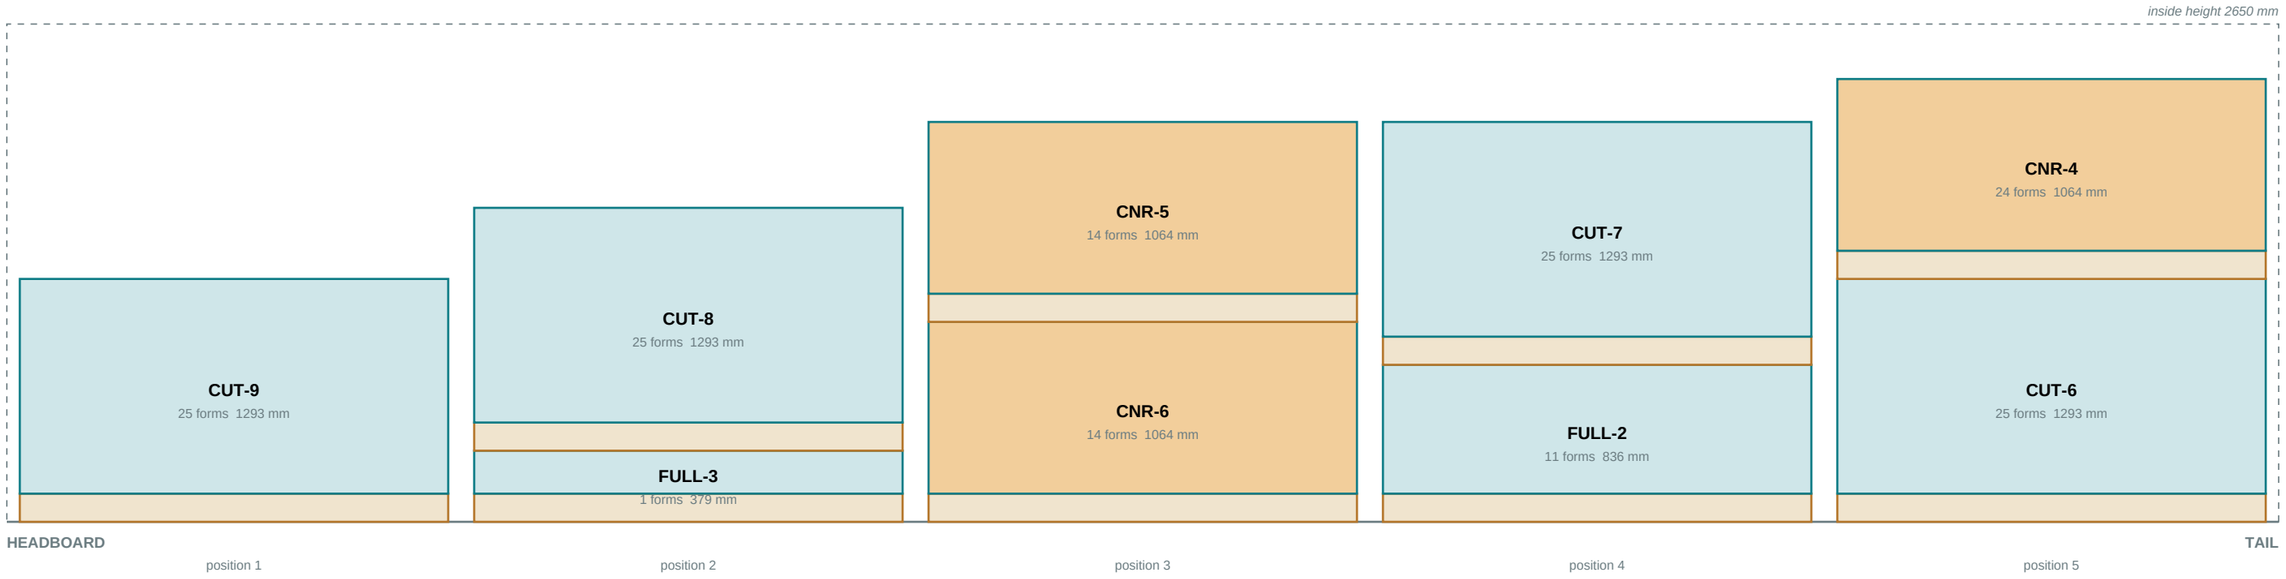

Unload order - 8 of 8 pallets come off out of build order, the price of stacking tallest forward

1. CNR-4 6in XR35 corners 24 forms courses L2 courses 1-3
2. CUT-6 6in XR35 straights 25 forms courses L2 courses 1-6
3. CUT-7 6in XR35 straights 25 forms courses L2 courses 2-6
4. FULL-2 6in XR35 straights 11 forms courses L2 courses 2-6
5. CNR-5 6in XR35 corners 14 forms courses L2 courses 4-6
6. CNR-6 6in XR35 corners 14 forms courses L3 courses 1-3
7. CUT-8 6in XR35 straights 25 forms courses L3 courses 1, 2, 3, 5, 6, 7, 8, 9
8. FULL-3 6in XR35 straights 1 forms courses L3 course 2
9. CUT-9 6in XR35 straights 25 forms courses L3 courses 3-10

Nudura™ **WAGON STACKING PLAN** **D2 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-065 Cuckfield Real Estate - Clifton, Bristol	FORMS	164
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	9	TALLEST	2357 mm
